

MEMORANDUM

TO: Programs, Projects and Operations Subcommittee
FROM: Martin P. Cleveland
SUBJECT: Silver Creek Watershed Sites #30 and #33 Repairs Project
Professional Services Agreement with Olsson, Inc.
DATE: August 23, 2021

The Silver Creek Watershed is located in Burt County, northwest of Tekamah, Nebr., as shown on the attached location map. Silver Creek Sites #30 and #33 have deficiencies that were found during the spring 2021 dam inspections by District staff and the Nebraska Department of Natural Resources Dam Safety Section staff. Attached are photos of these dam deficiencies. The structure deficiencies are as follows:

1. Silver Creek Site #30: Seepage flowing out of structure's downstream slope in numerous locations, including underneath the principal spillway pipe. The seepage needs to be intercepted by a filter, and conveyed to outlet channel in a safe manner and the principal spillway needs to be repaired; otherwise, the seepage may eventually lead to the structure failure.
2. Silver Creek Site #33: Full height slope sloughs on both sides of the structure principal spillway outlet plunge pool. These sloughs need to be stabilized to prevent potential damage to dam embankment and blockage of outlet channel flows.

The Silver Creek Watershed structures were originally designed by Olsson, Inc. (Site #30) and the Natural Resources Conservation Service (NRCS) (Site #33). Olsson, Inc. has provided design services for the Silver Creek Watershed Sites (dams) in the past and is familiar with the watershed and original structure designs. Therefore, staff believes they are the most qualified firm to provide the services needed to repair these dams.

Attached is a proposed professional services agreement with Olsson, Inc. for the Silver Creek Sites #30 and #33 Repairs Project. The tasks to be performed by Olsson, Inc. are as follows:

1. Geotechnical Exploration/Survey
2. Design and Plan Preparation
3. Bidding Documents
4. Construction Observation/Administration

The maximum not to exceed cost of the agreement is \$123,603. This amount is beyond the fee limit of \$50,000 for consultant selection without a Request for Proposals (RFP) as per Board Policy 15.2 Purchasing-Professional Services. Due to the fact that Olsson, Inc. is the most qualified to design repairs for Silver Creek Sites #30 and #33, staff recommends that the Board waive the RFP process and approve the proposed agreement with Olsson, Inc.

Management recommends that the Programs, Projects, and Operation Subcommittee recommend to the Board of Directors that Policy 15.2 Purchasing-Professional Services be waived and that the General Manager be authorized to execute the proposed Professional Services Agreement with Olsson, Inc. for the Silver Creek Watershed Sites #30 and #33 Repairs Project, with the maximum not to exceed amount of \$123,603, subject to changes deemed necessary by the General Manager and approval as to form by District Legal Counsel.

Silver Creek Watershed Burt County, Nebraska



Decatur

Lyons

Oakland

Craig

Tekamah

Herman

Thurston County
Burt County


Dodge County
Burt County

Burt County
Washington County

IOWA
NEBRASKA

Missouri River

IOWA
NEBRASKA

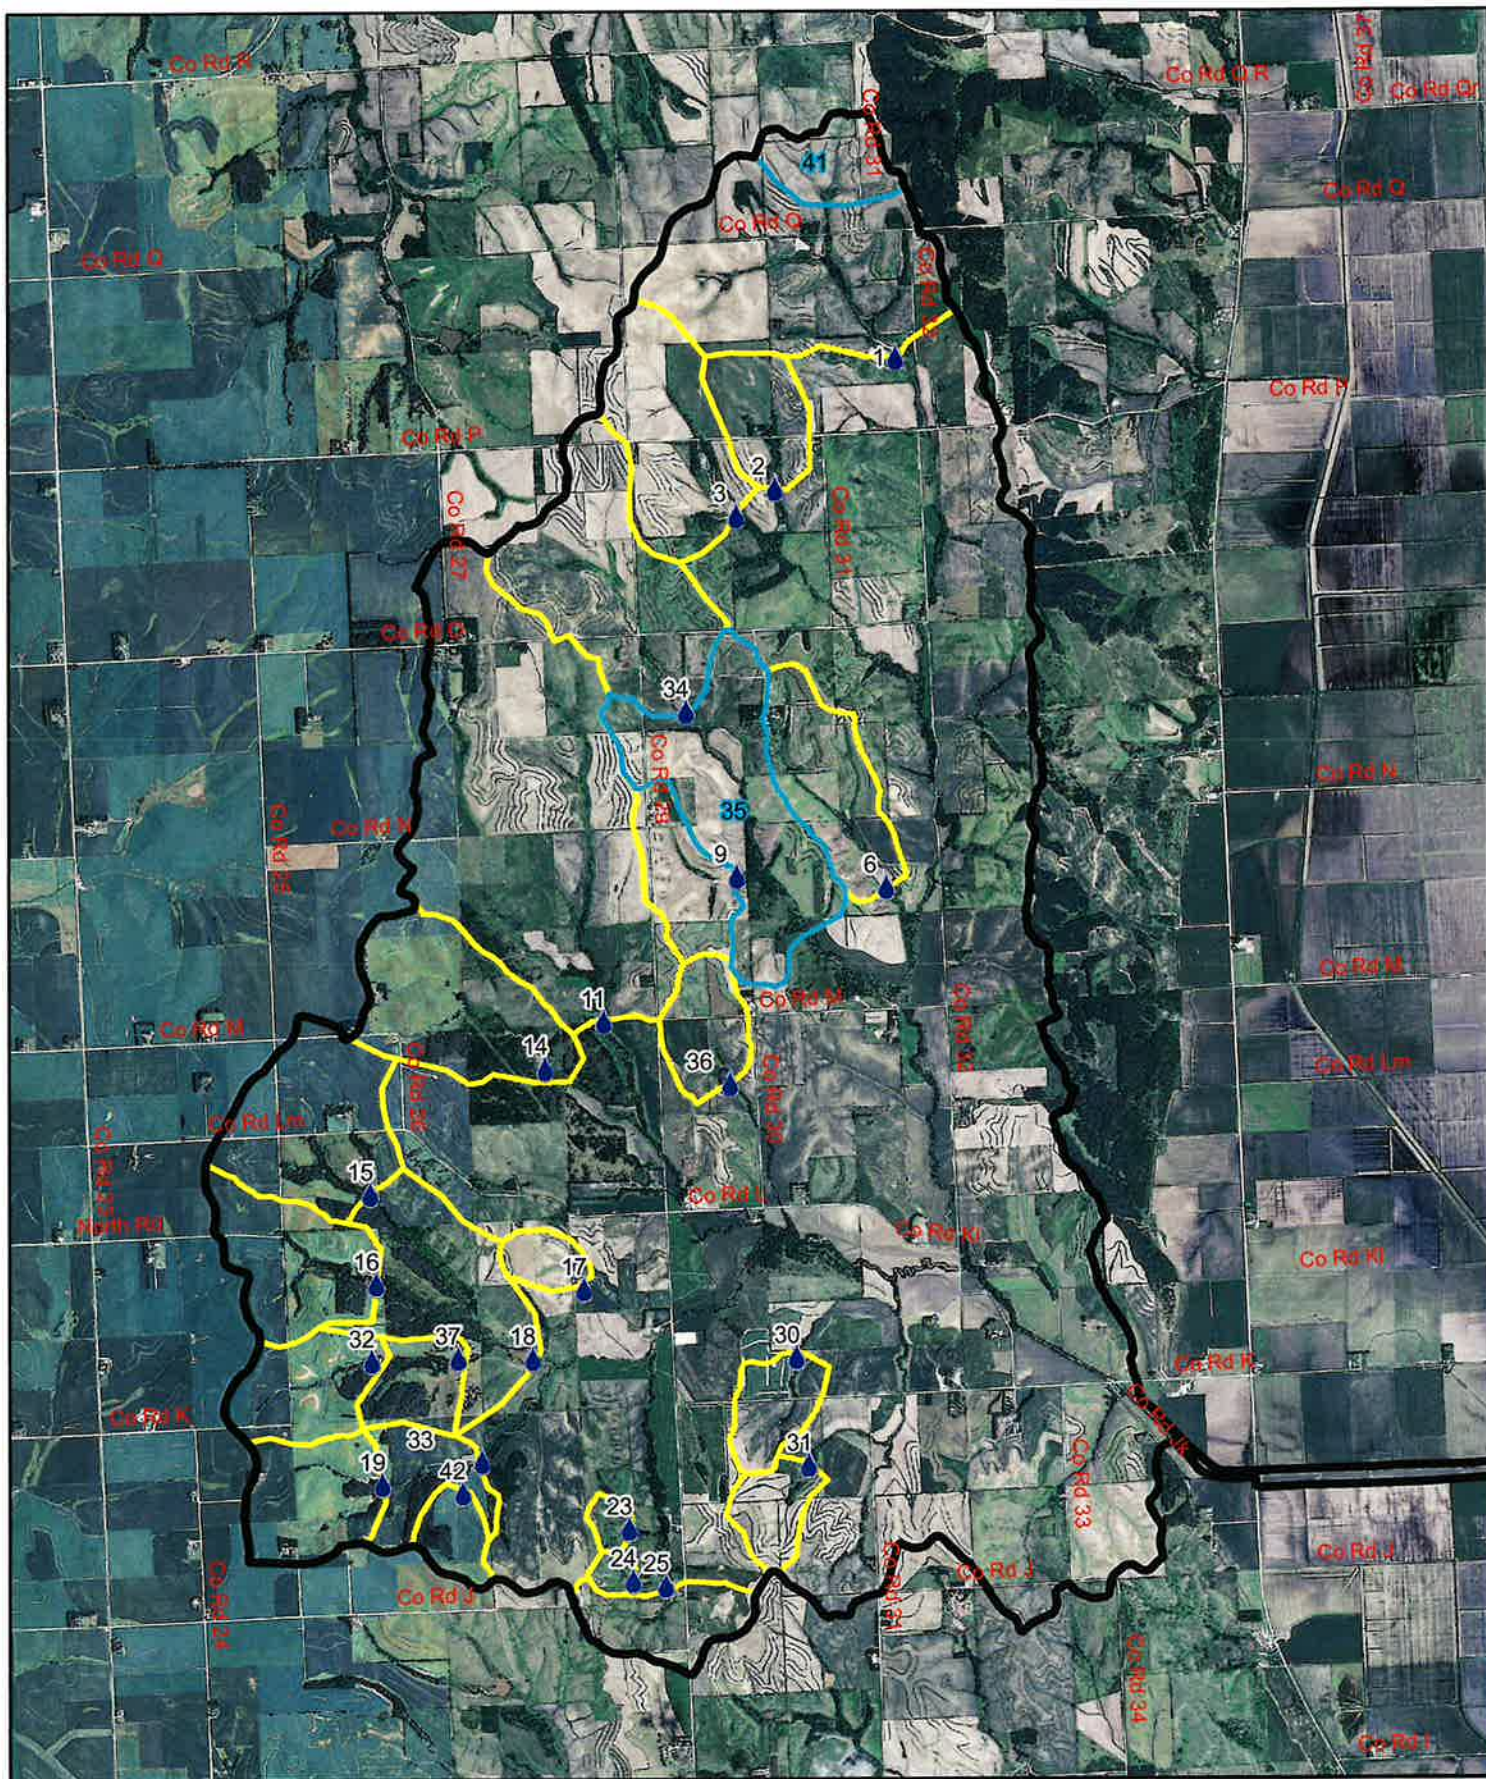


Structures

- Completed
- Deferred



SILVER CREEK WATERSHED



1 inch = 5,280 feet

Drawn By: Justin Novak
Date: 01/11/12

**Silver Creek Site #30 - Looking downstream at dam's
principal spillway outlet and downstream slope
April 2021**




Seepage areas

Dam Top



Silver Creek Site #33 - Looking downstream from dam top at outlet channel and sloughs
April 2021

Silver Creek #33 - Looking south at right bank slough
April 2021

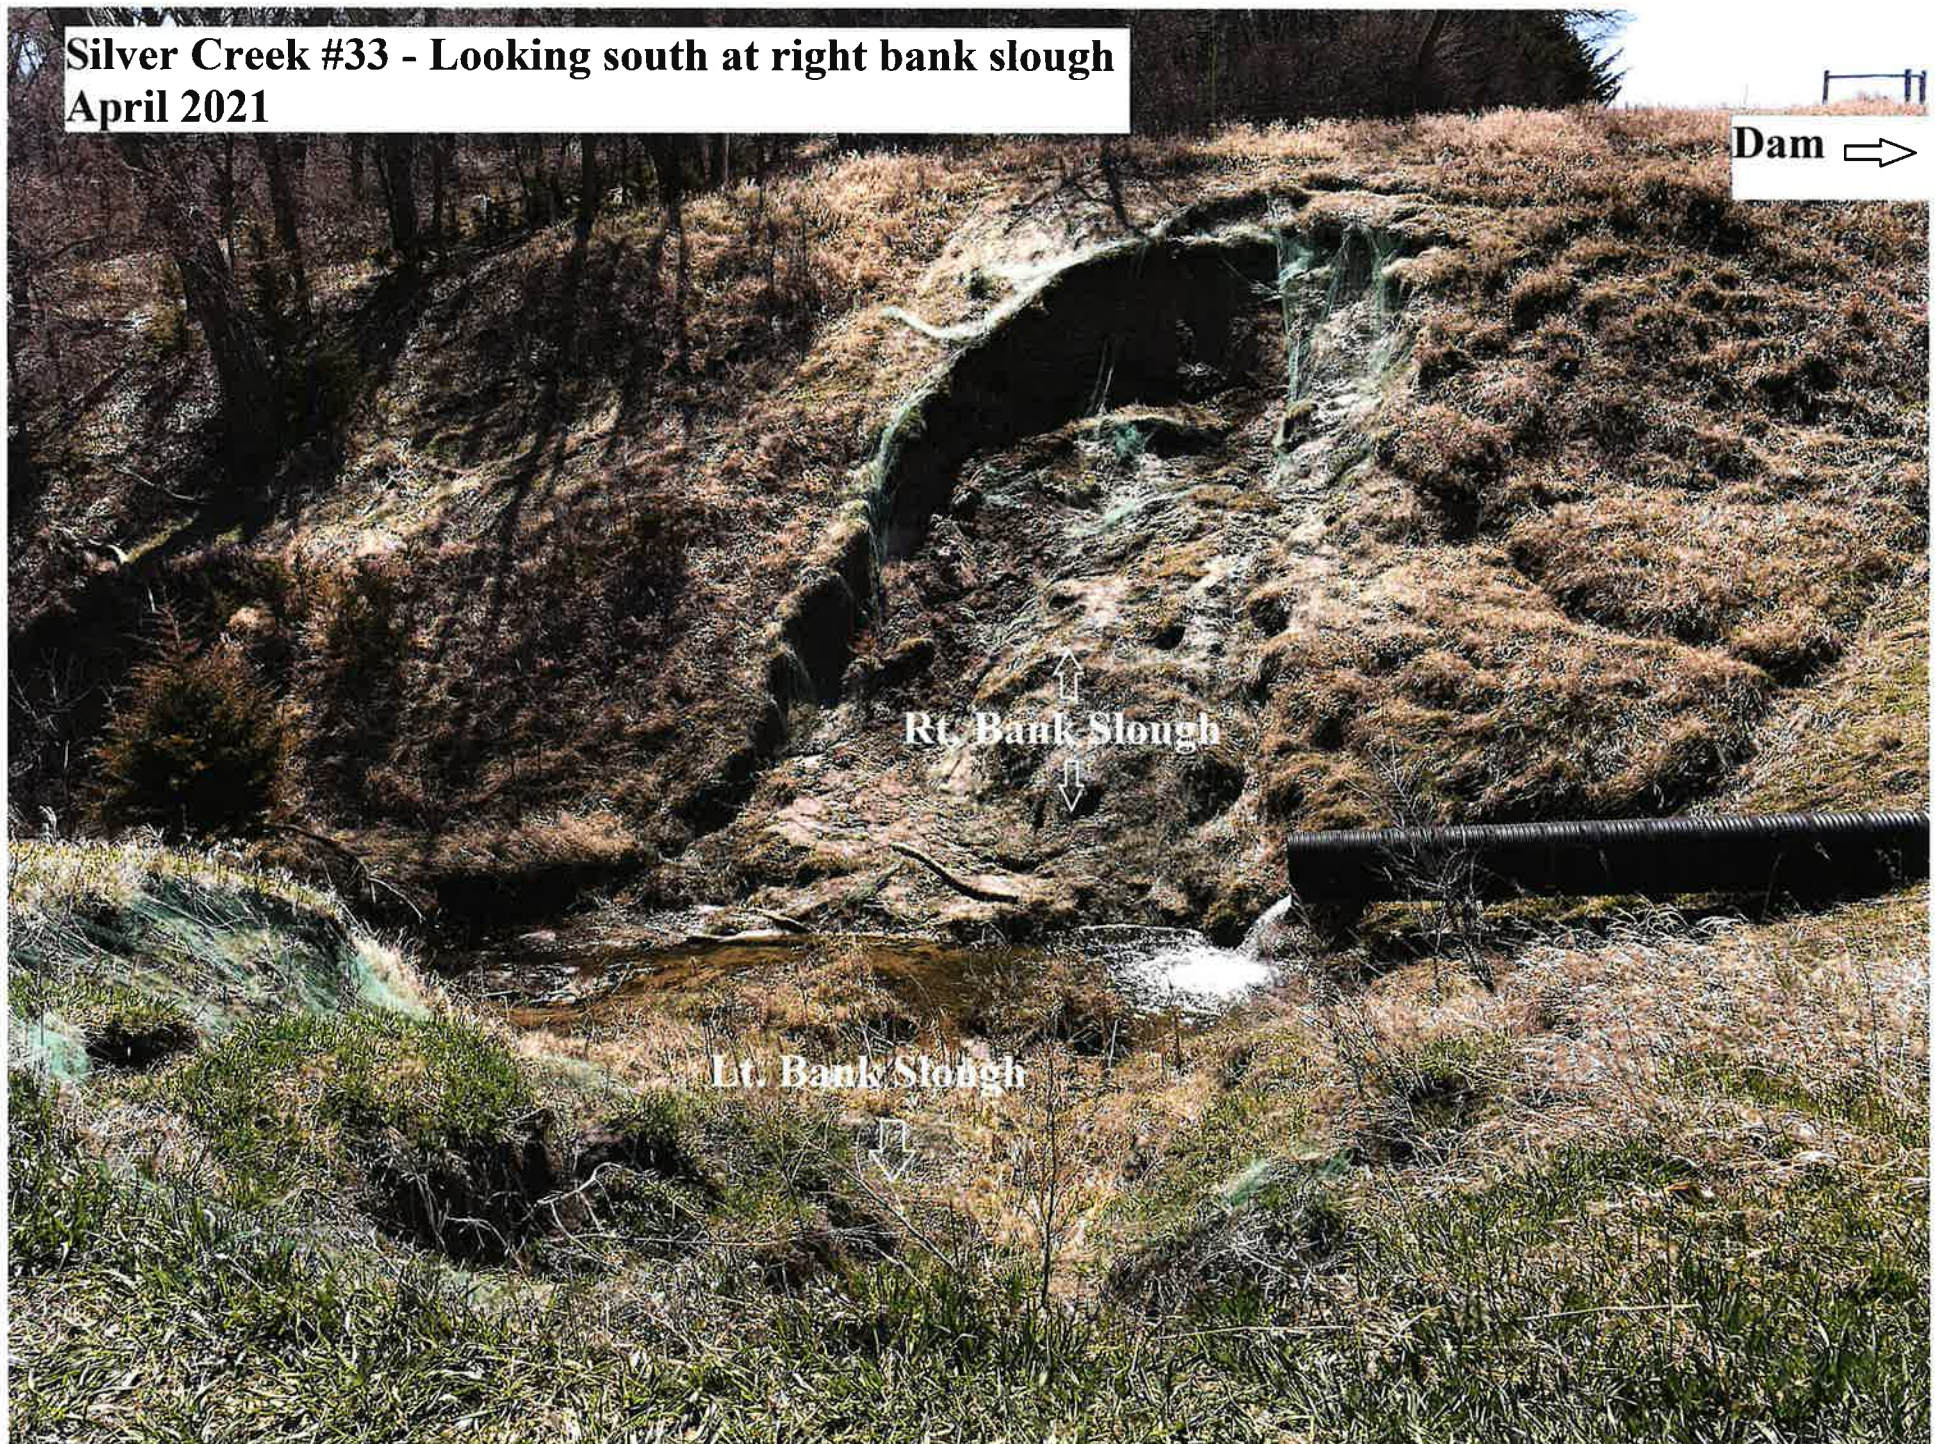

This document has important legal consequences; consultation with an attorney is encouraged with respect to its use or modification. This document should be adapted to the particular circumstances of the contemplated Project and the controlling Laws and Regulations.

AGREEMENT BETWEEN OWNER AND ENGINEER FOR PROFESSIONAL SERVICES

Original Version

Prepared by



Issued and Published Jointly by



MODIFIED VERSION

Papio-Missouri River Natural Resources District

A redline comparison copy of this document highlighting the changes made to the original version will be made available to you upon request.

*This document is a **MODIFIED VERSION** of*

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

This Agreement has been prepared for use with **EJCDC® C-700, Standard General Conditions of the Construction Contract, 2013 Edition**. Their provisions are interrelated, and a change in one may necessitate a change in the other. For guidance on the completion and use of this Agreement, see EJCDC® E-001, Commentary on the EJCDC Engineering Services Agreements, 2013 Edition.

NOTE: EJCDC publications may be purchased at www.ejcdc.org, or from any of the sponsoring organizations above.

TABLE OF CONTENTS

	<u>Page</u>
ARTICLE 1 – SERVICES OF ENGINEER	1
1.01 Scope	1
ARTICLE 2 – OWNER’S RESPONSIBILITIES	1
2.01 General.....	1
ARTICLE 3 – SCHEDULE FOR RENDERING SERVICES	2
3.01 Commencement	2
3.02 Time for Completion.....	2
ARTICLE 4 – INVOICES AND PAYMENTS.....	2
4.01 Invoices	2
4.02 Payments.....	3
ARTICLE 5 – OPINIONS OF COST	3
5.01 Opinions of Probable Construction Cost.....	3
5.02 Designing to Construction Cost Limit.....	4
5.03 Opinions of Total Project Costs	4
ARTICLE 6 – GENERAL CONSIDERATIONS	4
6.01 Standards of Performance.....	4
6.02 Design Without Construction Phase Services.....	6
6.03 Use of Documents	6
6.04 Electronic Transmittals	7
6.05 Insurance	7
6.06 Suspension and Termination.....	8
6.07 Controlling Law	9
6.08 Successors, Assigns, and Beneficiaries.....	9
6.09 Dispute Resolution.....	10
6.10 Environmental Condition of Site	10
6.11 Indemnification and Mutual Waiver	11
6.12 Records Retention	12
6.13 Miscellaneous Provisions	12
ARTICLE 7 – DEFINITIONS	13
7.01 Defined Terms.....	13
ARTICLE 8 – EXHIBITS AND SPECIAL PROVISIONS.....	18
8.01 Exhibits Included:.....	18
8.02 Total Agreement	18
8.03 Designated Representatives.....	18
8.04 Engineer's Certifications	19

*This document is a **MODIFIED VERSION** of*

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

**AGREEMENT
BETWEEN OWNER AND ENGINEER
FOR PROFESSIONAL SERVICES
(P-MRNRD MODIFIED)**

THIS IS AN AGREEMENT effective as of September 10, 2021 ("Effective Date") between
Papio-Missouri River Natural Resources District ("Owner") and
Olsson, Inc. ("Engineer").

Owner's Project, of which Engineer's services under this Agreement are a part, is generally identified as follows:

Silver Creek Watershed Sites 30 and 33 Repairs, Burt County, Nebraska ("Project").

Other terms used in this Agreement are defined in Article 7.

Engineer's services under this Agreement are generally identified as follows:

Project Management, Geotechnical Exploration, Plan Preparation, Construction Observation

Owner and Engineer further agree as follows:

ARTICLE 1 – SERVICES OF ENGINEER

1.01 Scope

- A. Engineer shall provide, or cause to be provided, the services set forth herein and in Exhibit A.

ARTICLE 2 – OWNER'S RESPONSIBILITIES

2.01 General

- A. Owner shall have the responsibilities set forth herein and in Exhibit B.
- B. Owner shall pay Engineer as set forth in Article 4 and Exhibit C.
- C. Owner shall be responsible for all requirements and instructions that it furnishes to Engineer pursuant to this Agreement, and for the accuracy and completeness of all programs, reports, data, and other information furnished by Owner to Engineer pursuant to this Agreement. Engineer may use and rely upon such requirements, programs, instructions, reports, data, and information in performing or furnishing services under this Agreement, subject to any express limitations or reservations applicable to the furnished items.
- D. Owner shall give written notice to Engineer as soon as reasonably practicable whenever Owner observes or otherwise becomes aware of:

*This document is a **MODIFIED VERSION** of*

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

1. any development that affects the scope or time of performance of Engineer's services;
2. the presence at the Site of any Constituent of Concern; or
3. any relevant, material defect or nonconformance in: (a) Engineer's services, (b) the Work, (c) the performance of any Constructor, or (d) Owner's performance of its responsibilities under this Agreement.

ARTICLE 3 – SCHEDULE FOR RENDERING SERVICES

3.01 Commencement

- A. Engineer is authorized to begin rendering services as of the Effective Date.

3.02 Time for Completion

- A. Engineer shall complete its obligations as expeditiously as is consistent with professional skill and care and the orderly progress of the Project, within a reasonable time. Specific periods of time for rendering services, or specific dates by which services are to be completed, are provided in Exhibit A, and are hereby agreed to be reasonable.
- B. If, through no fault of Engineer, such periods of time or dates are changed, or the orderly and continuous progress of Engineer's services is impaired, or Engineer's services are delayed or suspended and such changes or delays increase the time of performance of Engineer's services, then the time for completion of Engineer's services, and the rates and amounts of Engineer's compensation, shall be adjusted equitably.
- C. If Owner authorizes changes in the scope, extent, or character of the Project or Engineer's services in writing, then Owner shall pay Engineer compensation based on Engineer's normal hourly rates for time actually and necessarily devoted to services rendered in completing the additional services or shall negotiate an agreed upon fixed amount to perform such additional services, and the time for completion of Engineer's services shall be adjusted equitably, as agreed upon in writing by the parties.
- D. Owner shall make decisions and carry out its other responsibilities in a timely manner so as not to unreasonably delay the Engineer's performance of its services.
- E. If Engineer fails, through its own fault, to complete the performance required in this Agreement within the time set forth, as duly adjusted, then Owner shall be entitled, as its sole remedy, to the recovery of direct damages, if any, resulting from such failure in addition to any other remedies to which Owner may be entitled.

ARTICLE 4 – INVOICES AND PAYMENTS

4.01 Invoices

- A. *Preparation and Submittal of Invoices:* Engineer shall prepare invoices in accordance with its standard invoicing practices and the terms of Exhibit C. Engineer shall submit its invoices to Owner on a monthly basis by the last business day of the month. Invoices are

*This document is a **MODIFIED VERSION** of*

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

Page 2

due and payable within 45 days of receipt. Notwithstanding anything to the contrary, in no event shall Owner be obligated to make any payment, whether as compensation for services or relating to charges by consultants, reimbursement and/or otherwise, that would result in exceeding the Maximum Amount unless Owner otherwise agrees in a signed written agreement entered into pursuant to this Agreement.

4.02 *Payments*

- A. *Application to Interest and Principal:* Payment will be credited first to any interest owed to Engineer and then to principal.
- B. *Failure to Pay:* Subject to Paragraph 4.02.C, if Owner fails to make any payment due Engineer for services and expenses within 45 days after receipt of Engineer's invoice, then:
 - 1. amounts due Engineer will be increased at the rate of 1.0% per month (or the maximum rate of interest permitted by law, if less) from said thirtieth day; and
 - 2. Engineer may, after giving seven days written notice to Owner, suspend services under this Agreement until Owner has paid in full all amounts due for services, expenses, and other related charges. Owner waives any and all claims against Engineer for any such suspension.
- C. *Disputed Invoices:* If Owner disputes an invoice, either as to amount or entitlement, then Owner shall as soon as reasonably practicable, advise Engineer in writing of the specific basis for doing so, may withhold only that portion so disputed, and must pay the undisputed portion subject to the terms of Paragraph 4.01. Engineer shall continue performing services while any dispute is pending provided Owner has paid all undisputed amounts. Owner may withhold payment to the extent required to protect Owner from loss arising out of Engineer's performance or failure to perform any services.
- D. *Sales or Use Taxes:* If after the Effective Date of this Agreement any governmental entity takes a legislative action that imposes additional sales or use taxes on Engineer's services or compensation under this Agreement, then Engineer may invoice such additional sales or use taxes for reimbursement by Owner. Owner shall reimburse Engineer for the cost of such invoiced additional sales or use taxes; such reimbursement shall be in addition to the compensation to which Engineer is entitled under the terms of Exhibit C.

ARTICLE 5 – OPINIONS OF COST

5.01 *Opinions of Probable Construction Cost*

- A. Engineer's opinions (if any) of probable Construction Cost are to be made on the basis of Engineer's experience, qualifications, and general familiarity with the construction industry. However, because Engineer has no control over the cost of labor, materials, equipment, or services furnished by others, or over contractors' methods of determining prices, or over competitive bidding or market conditions, Engineer cannot and does not guarantee that proposals, bids, or actual Construction Cost will not vary from opinions of probable Construction Cost prepared by Engineer.

This document is a MODIFIED VERSION of

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

5.02 *Designing to Construction Cost Limit*

- A. If a Construction Cost limit is established between Owner and Engineer, such Construction Cost limit and a statement of Engineer's rights and responsibilities with respect thereto will be specifically set forth in Exhibit F to this Agreement.

5.03 *Opinions of Total Project Costs*

- A. The services, if any, of Engineer with respect to Total Project Costs shall be limited to assisting the Owner in tabulating the various categories that comprise Total Project Costs. Engineer assumes no responsibility for the accuracy of any opinions of Total Project Costs.

ARTICLE 6 – GENERAL CONSIDERATIONS

6.01 *Standards of Performance*

- A. *Standard of Care:* The standard of care for all professional engineering and related services performed or furnished by Engineer under this Agreement will be the care and skill ordinarily used by members of the subject profession currently practicing under similar circumstances at the same time and in Nebraska. Engineer makes no warranties, express or implied, under this Agreement or otherwise, in connection with any services performed or furnished by Engineer.
- B. *Technical Accuracy:* Owner shall not be responsible for discovering deficiencies in the technical accuracy of Engineer's services. Engineer shall correct deficiencies in technical accuracy without additional compensation unless such corrective action is directly and solely attributable to deficiencies in Owner-furnished information.
- C. *Consultants:* Engineer may retain such Consultants as Engineer deems necessary to assist in the performance or furnishing of the services, subject to reasonable, timely, and substantive objections by Owner.
- D. *Reliance on Others:* Subject to the standard of care set forth in Paragraph 6.01.A, Engineer and its Consultants may use or rely upon design elements and information ordinarily or customarily furnished by others, including, but not limited to, specialty contractors, manufacturers, suppliers, and the publishers of technical standards.
- E. *Compliance with Laws and Regulations, and Policies and Procedures:*
 - 1. Engineer and Owner shall comply with applicable Laws and Regulations.
 - 2. Owner's policies, procedures, performance standards and other information (collectively, the "Owner Policies") are accessible at <http://www.papionrd.org/about-nrd/policies-and-manuals/>. Engineer shall comply with any and all such Owner Policies and with any other instructions of Owner relating to Engineer's performance of services under this Agreement that Owner provides to Engineer in writing (collectively with Owner Policies, the "Owner Requirements"), subject to the standard of care set forth in Paragraph 6.01.A, and to the extent compliance is not inconsistent with professional practice requirements.

This document is a MODIFIED VERSION of

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

3. This Agreement is based on Laws and Regulations and Owner Requirements as of the Effective Date. The following may be the basis for modifications to Owner's responsibilities or to Engineer's scope of services, times of performance, or compensation, as applicable:
 - a. changes after the Effective Date to Laws and Regulations;
 - b. the receipt by Engineer after the Effective Date of new or different Owner Requirements.
4. Prior to the Effective Date, Engineer shall promptly notify Owner in writing of any objections to the Owner Requirements or conflicts between the Owner Requirements and Laws and Regulations and the parties shall use their best efforts to resolve such objections or conflicts.
- F. Engineer shall not be required to sign any document, no matter by whom requested, that would result in the Engineer having to certify, guarantee, or warrant the existence of conditions whose existence the Engineer cannot ascertain. Owner agrees not to make resolution of any dispute with the Engineer or payment of any amount due to the Engineer in any way contingent upon the Engineer signing any such document.
- G. The general conditions for any construction contract documents prepared hereunder are to be EJCDC® C-700 "Standard General Conditions of the Construction Contract" (2013 Edition), prepared by the Engineers Joint Contract Documents Committee and amended and/or supplemented by the parties (the "Standard General Conditions"), unless expressly indicated otherwise in Exhibit J or elsewhere in this Agreement.
- H. Engineer shall not at any time directly supervise, direct, control, or have authority over any Constructor's work, nor shall Engineer have direct authority over or be responsible for the means, methods, techniques, sequences, or procedures of construction selected or used by any Constructor, or the safety precautions and programs incident thereto, for security or safety at the Site, nor for any failure of a Constructor to comply with Laws and Regulations applicable to that Constructor's furnishing and performing of its work. Engineer shall not be responsible for the acts or omissions of any Constructor unless such action or omission is caused in whole or in part by Engineer.
- I. *Intentionally deleted.*
- J. Engineer shall not be responsible for any decision made regarding the Construction Contract Documents, or any application, interpretation, clarification, or modification of the Construction Contract Documents, other than those made or caused to be made by Engineer or its Consultants or other agents or representatives.
- K. Engineer is not required to provide and does not have any responsibility for surety bonding or insurance-related advice, recommendations, counseling, or research, or enforcement of construction insurance or surety bonding requirements except to the extent otherwise provided for in this Agreement, Addenda, the Contract Documents and/or any other agreement between Engineer and Owner.

- L. Engineer's services do not include providing legal advice or representation.
- M. Except to the extent otherwise agreed to by Owner and Engineer in writing, Engineer's services do not include (1) serving as a "municipal advisor" for purposes of the registration requirements of Section 975 of the Dodd-Frank Wall Street Reform and Consumer Protection Act (2010) or the municipal advisor registration rules issued by the Securities and Exchange Commission, or (2) advising Owner, or any municipal entity or other person or entity, regarding municipal financial products or the issuance of municipal securities, including advice with respect to the structure, timing, terms, or other similar matters concerning such products or issuances.
- N. While at the Site, Engineer, its Consultants, and their employees and representatives shall comply with the applicable requirements of Contractor's and Owner's safety programs. Engineer understands, acknowledges, and agrees that Engineer is responsible for ensuring that it, its Consultant, and their employees and representatives are aware and know of the applicable requirements of Contractor's and Owner's safety programs

6.02 *Design Without Construction Phase Services*

- A. Engineer shall be responsible only for those Construction Phase services expressly required of Engineer in Exhibit A, Paragraph A1.05. With the exception of such expressly required services, Engineer shall have no design, Shop Drawing review, or other obligations during construction, and Owner assumes all responsibility for the application and interpretation of the Construction Contract Documents, review and response to Contractor claims, Construction Contract administration, processing of Change Orders and submittals, revisions to the Construction Contract Documents during construction, construction observation and review, review of Contractor's payment applications, and all other necessary Construction Phase administrative, engineering, and professional services; and Owner waives only those claims against the Engineer directly connected thereto.

6.03 *Use of Documents*

- A. All Documents are instruments of service in respect to this Project, and shall become property of Owner without restriction or further limitation on their use, subject to receipt by Engineer of full payment for all services relating to preparation of the Documents and subject to Owner acknowledging that such documents are not intended or represented to be suitable for use on the Project unless completed by Engineer, or for use or reuse by Owner or others on extensions of the Project, on any other project, or for any other purpose, without written verification or adaptation by Engineer or another engineer. Engineer acknowledges that the Project is a public project subject to the Nebraska public record statutes, Neb. Rev. Stat. § 87-712, *et seq.*
- B. If Engineer is required to prepare or furnish Drawings or Specifications under this Agreement, Engineer shall deliver to Owner at least one original printed record version of such Drawings and Specifications, signed and sealed according to applicable Laws and Regulations. If requested by Owner, at no additional expense, Engineer shall make Documents available in an electronic format to be agreed upon by the parties.

This document is a MODIFIED VERSION of

- C. *Intentionally deleted.*
- D. If Engineer at Owner's request verifies the suitability of the Documents, completes them, or adapts them for extensions of the Project or for any other purpose, then Owner shall compensate Engineer at rates or in an amount to be agreed upon by Owner and Engineer.

6.04 *Electronic Transmittals*

- A. Owner and Engineer may transmit Project-related correspondence, Documents, text, data, drawings, information, and graphics, in electronic media or digital format, either directly, or through access to a secure Project website, in accordance with a mutually agreeable protocol.
- B. If this Agreement does not establish protocols for electronic or digital transmittals, then Owner and Engineer shall jointly develop such protocols.
- C. When transmitting items in electronic media or digital format, the transmitting party makes no representations as to long term compatibility, usability, or readability of the items resulting from the recipient's use of software application packages, operating systems, or computer hardware differing from those used in the drafting or transmittal of the items, or from those established in applicable transmittal protocols.

6.05 *Insurance*

- A. Engineer shall procure and maintain insurance as set forth in Exhibit G. Engineer shall cause Owner to be listed as an additional insured on any applicable general liability insurance policy carried by Engineer with a waiver of subrogation for such additional insureds.
- B. Owner shall procure and maintain insurance as set forth in Exhibit G. Owner shall cause Engineer and its Consultants to be listed as additional insureds on any general liability policies carried by Owner, which are applicable to the Project.
- C. Owner shall require Contractor to purchase and maintain general liability and other insurance in accordance with the requirements of Paragraph 6.03 of the "Standard General Conditions of the Construction Contract," No. C-700 (Rev. 1) as amended and/or supplemented by the parties, and shall cause Engineer and its Consultants to be listed as additional insureds with respect to such liability insurance purchased and maintained by Contractor for the Project.
- D. Owner and Engineer shall each deliver to the other certificates of insurance evidencing the coverages indicated in Exhibit G. Such certificates shall be furnished prior to commencement of Engineer's services and at renewals thereafter during the life of the Agreement.
- E. All policies of property insurance relating to the Project shall allow for waiver of subrogation rights and contain provisions to the effect that in the event of payment of any loss or damage the insurers will have no rights of recovery against any insured or additional insured thereunder or against Engineer or its Consultants.

This document is a MODIFIED VERSION of

- F. All policies of insurance shall contain a provision or endorsement that the coverage afforded will not be canceled or reduced in limits by endorsement, and that renewal will not be refused, until at least 10 days prior written notice has been given to the primary insured. Upon receipt of such notice, the receiving party shall promptly forward a copy of the notice to the other party to this Agreement.
- G. At any time, Owner may request that Engineer or its Consultants, at Owner's sole expense, provide additional insurance coverage, increased limits, or revised deductibles that are more protective than those specified in Exhibit G. If so, requested by Owner, and if commercially available, Engineer shall obtain and shall require its Consultants to obtain such additional insurance coverage, different limits, or revised deductibles for such periods of time as requested by Owner, and Exhibit G will be supplemented to incorporate these requirements.

6.06 *Suspension and Termination*

A. *Suspension:*

- 1. *By Owner:* Owner may suspend the Project upon seven days written notice to Engineer.
- 2. *By Engineer:* Subject to Paragraph 4.02.C, Engineer may, after giving seven days written notice to Owner, suspend services under this Agreement if Owner has failed to pay Engineer for undisputed invoiced services and expenses, as set forth in Paragraph 4.02.B, or in response to the presence of Constituents of Concern at the Site, as set forth in Paragraph 6.10.D.

B. *Termination:* The obligation to provide further services under this Agreement may be terminated:

- 1. For cause,
 - a. by Owner upon 7 days written notice if Engineer fails to fulfill in a timely and proper manner any of its obligations hereunder. Owner shall be entitled to withhold payment to Engineer until the Project is completed and the damages to Owner due to Engineer's default have been determined. Engineer shall be entitled to payment for the value of services performed less a deduction for the damages suffered by Owner as a result of the default.
 - b. by Engineer:
 - 1) upon seven days written notice if Owner demands that Engineer furnish or perform services contrary to Engineer's responsibilities as a licensed professional;
 - 2) upon seven days written notice if the Engineer's services for the Project are delayed or suspended for more than 120 days for reasons beyond Engineer's control; or
 - 3) as set forth in Paragraph 6.10.D.

This document is a MODIFIED VERSION of

- 4) Engineer shall have no liability to Owner on account of such termination.
- c. Notwithstanding the foregoing, this Agreement will not terminate under Paragraph 6.06.B.1.a if the party receiving such notice begins, within seven days of receipt of such notice, to correct its substantial failure to perform and proceeds diligently to cure such failure within no more than 7 days of receipt thereof; provided, however, that if and to the extent such substantial failure cannot be reasonably cured within such 7 day period, and if such party has diligently attempted to cure the same and thereafter continues diligently to cure the same, then the cure period provided for herein shall extend up to, but in no case more than, 30 days after the date of receipt of the notice.
2. For convenience, by Owner for any reason or no reason and with or without cause effective upon Engineer's receipt of notice from Owner.
- C. *Effective Date of Termination:* The terminating party under Paragraph 6.06.B may set the effective date of termination at a time up to 30 days later than otherwise provided to allow Engineer to demobilize personnel and equipment from the Site, to complete tasks whose value would otherwise be lost, to prepare notes as to the status of completed and uncompleted tasks, and to assemble Project materials in orderly files.
- D. *Payments Upon Termination:*
 1. In the event of any termination under Paragraph 6.06, Engineer will be entitled to invoice Owner and to receive full payment for all services performed or furnished in accordance with this Agreement and all Reimbursable Expenses incurred through the effective date of termination. Upon making such payment, Owner shall have full ownership and rights to use of Documents, at Owner's sole risk, subject to the provisions of Paragraph 6.03.
 2. In the event of termination by Owner for convenience or by Engineer for cause, Engineer shall be entitled, in addition to invoicing for those items identified in Paragraph 6.06.D.1, to invoice Owner and receive payment of a reasonable amount for services and expenses directly attributable to termination, both before and after the effective date of termination, such as reassignment of personnel, costs of terminating contracts with Engineer's Consultants, and other related close-out costs, using methods and rates for Additional Services as set forth in Exhibit C and incurred prior to the effective date of the termination. Under no circumstances shall Owner be responsible for Engineer's indirect or consequential damages, including, but not limited to, lost or anticipated profits.

6.07 Controlling Law

- A. This Agreement is to be governed by the Laws and Regulations of the state of Nebraska.

6.08 Successors, Assigns, and Beneficiaries

- A. Owner and Engineer and the successors, executors, administrators, and legal representatives of Owner and Engineer (and to the extent permitted by Paragraph 6.08.B the assigns of Owner and Engineer) are hereby bound to the other party to this

*This document is a **MODIFIED VERSION** of*

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

Agreement and to the successors, executors, administrators, and legal representatives (and said assigns) of such other party, in respect of all covenants, agreements, and obligations of this Agreement.

- B. Engineer may not assign, sublet, or transfer any rights under or interest (including, but without limitation, money that is due or may become due) in this Agreement without the written consent of Owner, except to the extent that any assignment, subletting, or transfer is mandated by law. Unless specifically stated to the contrary in any written consent to an assignment, no assignment will release or discharge Engineer from any duty or responsibility under this Agreement.
- C. Unless expressly provided otherwise in this Agreement:
 - 1. Nothing in this Agreement shall be construed to create, impose, or give rise to any duty owed by Owner or Engineer to any Constructor, other third-party individual or entity, or to any surety for or employee of any of them.
 - 2. All duties and responsibilities undertaken pursuant to this Agreement will be for the sole and exclusive benefit of Owner and Engineer and not for the benefit of any other party.
 - 3. Owner agrees that the substance of the provisions of this Paragraph 6.08.C shall appear in the Construction Contract Documents.

6.09 *Dispute Resolution*

- A. Owner and Engineer agree to negotiate all disputes between them in good faith for a period of 30 days from the date of notice prior to invoking the procedures of Exhibit H or other provisions of this Agreement, or exercising their rights at law.
- B. If the parties fail to resolve a dispute through negotiation under Paragraph 6.09.A, then either or both may invoke the procedures of Exhibit H. If Exhibit H is not included, or if no dispute resolution method is specified in Exhibit H, then the parties may exercise their rights at law.

6.10 *Environmental Condition of Site*

- A. Owner represents to Engineer that as of the Effective Date to the best of Owner's knowledge no Constituents of Concern, other than those disclosed in writing to Engineer, exist at the Site.
- B. If Engineer encounters or learns of an undisclosed Constituent of Concern at the Site, then Engineer shall notify (1) Owner and (2) appropriate governmental officials if Engineer reasonably concludes that doing so is required by applicable Laws or Regulations.
- C. It is acknowledged by both parties that Engineer's scope of services does not include any services related to unknown or undisclosed Constituents of Concern. If Engineer or any other party encounters, uncovers, or reveals an undisclosed Constituent of Concern, or if investigative or remedial action, or other professional services, are necessary with respect to undisclosed Constituents of Concern, then Engineer may, at its option and without

This document is a MODIFIED VERSION of

liability, suspend performance of services on the portion of the Project affected thereby until Owner: (1) retains appropriate specialist consultant(s) or contractor(s) to identify and, as appropriate, abate, remediate, or remove the Constituents of Concern; and (2) warrants that the Sire is in full compliance with applicable Laws and Regulations.

- D. If the presence at the Site of undisclosed Constituents of Concern adversely affects the performance of Engineer's services under this Agreement, then the Engineer shall have the option of (1) accepting an equitable adjustment in its compensation or in the time of completion, or both; or (2) terminating this Agreement for cause on 30 days notice.
- E. Owner acknowledges that Engineer is performing professional services for Owner and that Engineer is not and shall not be required to become an "owner," "arranger," "operator," "generator," or "transporter" of hazardous substances, as defined in the Comprehensive Environmental Response, Compensation, and Liability Act (CERCLA), as amended, which are or may be encountered at or near the Site in connection with Engineer's activities under this Agreement.

6.11 *Indemnification and Mutual Waiver*

- A. *Indemnification by Engineer:* To the fullest extent permitted by Laws and Regulations, Engineer shall indemnify and hold harmless Owner, and Owner's officers, directors, members, managers, partners, agents, consultants, and employees, from and against any and all claims, costs, losses, damages, and judgments (including, but not limited to, all fees and charges of engineers, architects, attorneys, and other professionals, and all court, arbitration, or other dispute resolution costs) arising out of or relating to this Agreement and/or the Project, provided that any such claim, cost, loss, damages, or judgment is attributable to bodily injury, sickness, disease, or death, or to injury to or destruction of tangible property (other than the Work itself), including the loss of use resulting therefrom, but only to the extent caused by any negligent act or omission or intentional misconduct of Engineer or Engineer's principals, officers, directors, managers, members, partners, agents, employees, or Consultants or other representatives.
- B. *Indemnification by Owner:* To the extent permitted by Laws and Regulations, Owner shall indemnify and hold harmless Engineer and its officers, directors, members, partners, agents, employees, and Consultants from and against any and all claims, costs, losses, damages, and judgments (including, but not limited to, all fees and charges of engineers, architects, attorneys, and other professionals, and all court, arbitration, or other dispute resolution costs) arising out of or relating to this Agreement and/or the Project, provided that any such claim, cost, loss, damages, or judgment is directly attributable to bodily injury, sickness, disease, or death, or to injury to or destruction of tangible property (other than the Work itself), including the loss of use resulting therefrom, but only to the extent caused by any negligent act or omission or intentional misconduct of Owner or Owner's officers, directors or employees with respect to this Agreement or to the Project.
- C. *Environmental Indemnification:* To the fullest extent permitted by Laws and Regulations, Owner shall indemnify and hold harmless Engineer and its officers, directors, members, partners, agents, employees, and Consultants from all claims, costs, losses, damages, actions, and judgments (including reasonable consultants' and attorney's fees and

expenses) caused by, arising out of, relating to, or resulting from a Constituent of Concern at, on, or under the Site, provided that (1) any such claim, cost, loss, damages, action, or judgment is attributable to bodily injury, sickness, disease, or death, or to injury to or destruction of tangible property (other than the Work itself), including the loss of use resulting therefrom, and (2) nothing in this paragraph shall obligate Owner to indemnify any individual or entity from and against the consequences of that individual's or entity's own negligence or willful misconduct.

- D. *No Defense Obligation:* The indemnification commitments in this Agreement do not include a defense obligation by the indemnitor unless such obligation is expressly stated.
- E. *Intentionally deleted.*
- F. *Mutual Waiver:* To the fullest extent permitted by Laws and Regulations, Owner and Engineer waive against each other, and the other's employees, officers, directors, members, agents, insurers, partners, and consultants, any and all claims for or entitlement to special, incidental, indirect, or consequential damages arising out of, resulting from, or in any way related to this Agreement or the Project, from any cause or causes; provided, however, that this waiver does not apply to restrict or limit available insurance or indemnity claims arising from third-party claims.

6.12 *Records Retention*

- A. Engineer shall maintain on file in legible form, for a period of five years following completion or termination of its services, all Documents, records (including cost records), and design calculations related to Engineer's services or pertinent to Engineer's performance under this Agreement. Upon Owner's request, Engineer shall provide a copy of any such item to Owner at no cost to Owner.

6.13 *Miscellaneous Provisions*

- A. *Notices:* Any notice required under this Agreement will be in writing, addressed to the appropriate party at its address on the signature page and given personally, by facsimile, by registered or certified mail postage prepaid, or by a commercial courier service. All notices shall be effective upon the date of receipt.
- B. *Survival:* All express representations, waivers, indemnifications, and limitations of liability included in this Agreement will survive its completion or termination for any reason.
- C. *Severability:* Any provision or part of the Agreement held to be void or unenforceable under any Laws or Regulations shall be deemed stricken, and all remaining provisions shall continue to be valid and binding upon Owner and Engineer, which agree that the Agreement shall be reformed to replace such stricken provision or part thereof with a valid and enforceable provision that comes as close as possible to expressing the intention of the stricken provision.
- D. *Waiver:* A party's non-enforcement of any provision shall not constitute a waiver of that provision, nor shall it affect the enforceability of that provision or of the remainder of this Agreement.

*This document is a **MODIFIED VERSION** of*

- E. *Accrual of Claims:* To the fullest extent permitted by Laws and Regulations, all causes of action arising under this Agreement shall be deemed to have accrued, and all statutory periods of limitation shall commence, no later than the date of Substantial Completion.
- F. *Non-Discrimination.* Engineer shall not discriminate against any employee or applicant for employment, to be employed in the performance of the Project, with respect to his/her hire, tenure, terms, conditions, or privileges of employment, because of his or her race, color, religion, sex, disability, or national origin.
- G. *Ethics in Public Contracting.* Engineer represents and warrants that it has not and will not pay or offer to pay, either directly or indirectly, any fee, commission compensation, gift, gratuity, or anything of value to any Nebraska or other government officer, board member, employee or evaluator based on the understanding that the receiving person's vote, actions, or judgment will be influenced thereby. Engineer further represents and warrants that it is prohibited from utilizing the services of lobbyists, attorneys, political activists, or consultants to secure any contract in any way relating to the Project. It is the intent of this Paragraph 6.13.F to assure that the prohibition of government contact during the procurement process is not subverted through the use of lobbyists, attorneys, political activists, or consultants. It is the intent of the Owner that the process of evaluation of proposals and award of the Work and the Project be completed without external influence. It is not the intent of this Paragraph 6.13.F to prohibit any party from seeking professional advice, for example consulting legal counsel, regarding terms and conditions of this or any other contract or agreement or proposal. Engineer may not refer to receiving the award of this Agreement or the Project in advertising in such a manner as to state or imply that it or its services are endorsed or preferred by Owner. News releases pertaining to the Work shall not be issued without prior written approval from Owner. If Engineer is found to be in non-compliance with this Paragraph 6.13.F, Engineer may forfeit the Agreement and the Project and any contract or other agreement relating to the Project awarded to it.
- H. *Sovereign Immunity.* Nothing in this Agreement or in any other agreement between the parties shall be construed as a waiver of all or any part of, or as in any way limited, the sovereign immunity afforded to Owner pursuant to Laws and Regulations.

ARTICLE 7 – DEFINITIONS

7.01 *Defined Terms*

- A. Wherever used in this Agreement (including the Exhibits hereto) terms (including the singular and plural forms) printed with initial capital letters have the meanings indicated in the text above, in the exhibits, in the following provisions, in the Standard General Conditions, or in the following definitions:
 - 1. *Addenda*—Written or graphic instruments issued prior to the opening of bids which clarify, correct, or change the bidding requirements or the proposed Construction Contract Documents.

This document is a MODIFIED VERSION of

2. *Additional Services*—The services to be performed for or furnished to Owner by Engineer in accordance with Part 2 of Exhibit A of this Agreement.
3. *Agreement*—This written contract for professional services between Owner and Engineer, including all exhibits identified in Paragraph 8.01 and any duly executed amendments.
4. *Application for Payment*—The form acceptable to Owner and Engineer which is to be used by Contractor during the course of the Work in requesting progress or final payments and which is to be accompanied by such supporting documentation as is required by the Construction Contract.
5. *Basic Services*—The services to be performed for or furnished to Owner by Engineer in accordance with Part 1 of Exhibit A of this Agreement.
6. *Change Order*—A document which is signed by Contractor and Owner and authorizes an addition, deletion, or revision in the Work or an adjustment in the Construction Contract Price or the Construction Contract Times, or other revision to the Construction Contract, issued on or after the effective date of the Construction Contract.
7. *Change Proposal*—A written request by Contractor, duly submitted in compliance with the procedural requirements set forth in the Construction Contract, seeking an adjustment in Construction Contract Price or Construction Contract Times, or both; contesting an initial decision by Engineer concerning the requirements of the Construction Contract Documents or the acceptability of Work under the Construction Contract Documents; challenging a set-off against payments due; or seeking other relief with respect to the terms of the Construction Contract.
8. *Constituent of Concern*—Asbestos, petroleum, radioactive material, polychlorinated biphenyls (PCBs), hazardous waste, and any substance, product, waste, or other material of any nature whatsoever that is or becomes listed, regulated, or addressed pursuant to (a) the Comprehensive Environmental Response, Compensation and Liability Act, 42 U.S.C. §§9601 et seq. (“CERCLA”); (b) the Hazardous Materials Transportation Act, 49 U.S.C. §§5501 et seq.; (c) the Resource Conservation and Recovery Act, 42 U.S.C. §§6901 et seq. (“RCRA”); (d) the Toxic Substances Control Act, 15 U.S.C. §§2601 et seq.; (e) the Clean Water Act, 33 U.S.C. §§1251 et seq.; (f) the Clean Air Act, 42 U.S.C. §§7401 et seq.; or (g) any other federal, State, or local statute, law, rule, regulation, ordinance, resolution, code, order, or decree regulating, relating to, or imposing liability or standards of conduct concerning, any hazardous, toxic, or dangerous waste, substance, or material.
9. *Construction Contract*—The entire and integrated written contract between the Owner and Contractor concerning the Work.
10. *Construction Contract Documents*—Those items designated as “Contract Documents” in the Construction Contract, and which together comprise the Construction Contract.

This document is a MODIFIED VERSION of

11. *Construction Contract Price*—The money that Owner has agreed to pay Contractor for completion of the Work in accordance with the Construction Contract Documents.
12. *Construction Contract Times*—The number of days or the dates by which Contractor shall: (a) achieve milestones, if any, in the Construction Contract; (b) achieve Substantial Completion; and (c) complete the Work.
13. *Construction Cost*—The cost to Owner of the construction of those portions of the entire Project designed or specified by or for Engineer under this Agreement, including construction labor, services, materials, equipment, insurance, and bonding costs, and allowances for contingencies. Construction Cost does not include costs of services of Engineer or other design professionals and consultants; cost of land or rights-of-way, or compensation for damages to property; Owner's costs for legal, accounting, insurance counseling, or auditing services; interest or financing charges incurred in connection with the Project; or the cost of other services to be provided by others to Owner. Construction Cost is one of the items comprising Total Project Costs.
14. *Constructor*—Any person or entity (not including the Engineer, its employees, agents, representatives, and Consultants), performing or supporting construction activities relating to the Project, including but not limited to Contractors, Subcontractors, Suppliers, Owner's work forces, utility companies, other contractors, construction managers, testing firms, shippers, and truckers, and the employees, agents, and representatives of any or all of them.
15. *Consultants*—Individuals or entities having a contract or other arrangement with Engineer to furnish services with respect to this Project.
16. *Contractor*—The entity or individual with which Owner enters into a Construction Contract.
17. *Day*—A calendar day of 24 hours measured from midnight to the next midnight.
18. *Documents*—Data, reports, Drawings, Specifications, Record Drawings, building information models, civil integrated management models, and other deliverables, whether in printed or electronic format, provided or furnished in appropriate phases by Engineer to Owner pursuant to this Agreement.
19. *Drawings*—That part of the Construction Contract Documents that graphically shows the scope, extent, and character of the proposed Work to be performed by Contractor in accordance with and for the benefit of the Project.
20. *Effective Date*—The date indicated in this Agreement on which it becomes effective, but if no such date is indicated, the date on which this Agreement is signed and delivered by the last of the parties to sign and deliver.
21. *Engineer*—The individual or entity named as such in this Agreement.

22. *Field Order*—A written order issued by Engineer which requires minor changes in the Work but does not change the Construction Contract Price or the Construction Contract Times.
23. *Laws and Regulations; Laws or Regulations*—Any and all applicable laws, statutes, rules, regulations, ordinances, codes, and orders of any and all governmental bodies, agencies, authorities, and courts having jurisdiction.
24. *Maximum Amount*—The aggregate amount of one hundred and twenty-three thousand, six hundred three dollars (\$123,603.00), which is the maximum to be paid by Owner with respect to and/or pursuant to this Agreement under any and all circumstances unless Owner agrees otherwise in a signed written agreement entered into pursuant to this Agreement.
25. *Owner*—The individual or entity named as such in this Agreement and for which Engineer's services are to be performed. Unless indicated otherwise, this is the same individual or entity that will enter into any Construction Contracts concerning the Project.
26. *Project*—As defined on the first page of this Agreement, and including the total undertaking to be accomplished for Owner by engineers, contractors, and others, including planning, study, design, construction, testing, commissioning, and start-up, and of which the services to be performed or furnished by Engineer under this Agreement are a part.
27. *Record Drawings*—Drawings depicting the completed Project, or a specific portion of the completed Project, prepared by Engineer as an Additional Service and based on Contractor's record copy of all Drawings, Specifications, Addenda, Change Orders, Work Change Directives, Field Orders, and written interpretations and clarifications, as delivered to Engineer and annotated by Contractor to show changes made during construction.
28. *Reimbursable Expenses*—The expenses incurred reasonably and directly by Engineer in connection with the performing or furnishing of Basic Services and Additional Services for the Project, as detailed in Exhibit C.
29. *Resident Project Representative*—The authorized representative of Engineer, if any, assigned to assist Engineer at the Site during the Construction Phase. The Resident Project Representative will be Engineer's agent or employee and under Engineer's supervision. As used herein, the term Resident Project Representative or "RPR" includes any assistants or field staff of Resident Project Representative. The duties and responsibilities of the Resident Project Representative, if any, are as set forth in Exhibit D.
30. *Samples*—Physical examples of materials, equipment, or workmanship that are representative of some portion of the Work and that establish the standards by which such portion of the Work will be judged.

This document is a MODIFIED VERSION of

31. *Shop Drawings*—All drawings, diagrams, illustrations, schedules, and other data or information that are specifically prepared or assembled by or for Contractor and submitted by Contractor to illustrate some portion of the Work. Shop Drawings, whether approved or not, are not Drawings and are not Construction Contract Documents.
32. *Site*—Lands or areas to be indicated in the Construction Contract Documents as being furnished by Owner upon which the Work is to be performed, including rights-of-way and easements, and such other lands furnished by Owner which are designated for the use of Contractor.
33. *Specifications*—The part of the Construction Contract Documents that consists of written requirements for materials, equipment, systems, standards, and workmanship as applied to the Work, and certain administrative requirements and procedural matters applicable to the Work.
34. *Subcontractor*—An individual or entity having a direct contract with Contractor or with any other Subcontractor for the performance of a part of the Work.
35. *Substantial Completion*—The time at which the Work (or a specified part thereof) has progressed to the point where, in the opinion of Engineer, the Work (or a specified part thereof) is sufficiently complete, in accordance with the Construction Contract Documents, so that the Work (or a specified part thereof) can be utilized for the purposes for which it is intended. The terms “substantially complete” and “substantially completed” as applied to all or part of the Work refer to Substantial Completion thereof.
36. *Supplier*—A manufacturer, fabricator, supplier, distributor, materialman, or vendor having a direct contract with Contractor or with any Subcontractor to furnish materials or equipment to be incorporated in the Work by Contractor or a Subcontractor.
37. *Total Project Costs*—The total cost of planning, studying, designing, constructing, testing, commissioning, and start-up of the Project, including Construction Cost and all other Project labor, services, materials, equipment, insurance, and bonding costs, allowances for contingencies, and the total costs of services of Engineer or other design professionals and consultants, together with such other Project-related costs that Owner furnishes for inclusion, including but not limited to cost of land, rights-of-way, compensation for damages to properties, Owner’s costs for legal, accounting, insurance counseling, and auditing services, interest and financing charges incurred in connection with the Project, and the cost of other services to be provided by others to Owner.
38. *Work*—The entire construction or the various separately identifiable parts thereof required to be provided under the Construction Contract Documents. Work includes and is the result of performing or providing all labor, services, and documentation necessary to produce such construction; furnishing, installing, and incorporating all materials and equipment into such construction; and may include related services such as testing, start-up, and commissioning, all as required by the Construction Contract Documents.

39. *Work Change Directive*—A written directive to Contractor issued on or after the effective date of the Construction Contract, signed by Owner and recommended by Engineer, ordering an addition, deletion, or revision in the Work.

ARTICLE 8 – EXHIBITS AND SPECIAL PROVISIONS

8.01 Exhibits Included:

- A. Exhibit A, Engineer's Services.
- B. Exhibit B, Owner's Responsibilities.
- C. Exhibit C, Payments to Engineer for Services and Reimbursable Expenses.
- D. Exhibit D, Duties, Responsibilities and Limitations of Authority of Resident Project Representative.
- E. Exhibit E, Notice of Acceptability of Work.
- ~~F. Exhibit F, Construction Cost Limit. NOT USED.~~
- G. Exhibit G, Insurance.
- H. Exhibit H, Dispute Resolution.
- ~~I. Exhibit I, Limitations of Liability. NOT USED.~~
- J. Exhibit J, Special Provisions.
- K. Exhibit K, Amendment to Owner-Engineer Agreement.

8.02 Total Agreement

- A. This Agreement, (together with the exhibits included above) constitutes the entire agreement between Owner and Engineer and supersedes all prior written or oral understandings. This Agreement may only be amended, supplemented, modified, or canceled by a written instrument duly executed by both parties. Amendments should be based whenever possible on the format of Exhibit K to this Agreement.

8.03 Designated Representatives

- A. With the execution of this Agreement, Engineer and Owner shall designate specific individuals to act as Engineer's and Owner's representatives with respect to the services to be performed or furnished by Engineer and responsibilities of Owner under this Agreement. Such an individual shall have authority to transmit instructions, receive information, and render decisions relative to this Agreement on behalf of the respective party whom the individual represents.

*This document is a **MODIFIED VERSION** of*

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

8.04 *Engineer's Certifications*

- A. Engineer certifies that it has not engaged in corrupt, fraudulent, or coercive practices in competing for or in executing the Agreement. For the purposes of this Paragraph 8.04:
1. "corrupt practice" means the offering, giving, receiving, or soliciting of anything of value likely to influence the action of a public official in the selection process or in the Agreement execution;
 2. "fraudulent practice" means an intentional misrepresentation of facts made (a) to influence the selection process or the execution of the Agreement to the detriment of Owner, or (b) to deprive Owner of the benefits of free and open competition;
 3. "coercive practice" means harming or threatening to harm, directly or indirectly, persons or their property to influence their participation in the selection process or affect the execution of the Agreement.

IN WITNESS WHEREOF, the parties hereto have executed this Agreement, the Effective Date of which is indicated on page 1.

Owner:
Papio-Missouri River Natural Resources District

Engineer:
Olsson, Inc.

By: _____
Print name: John Winkler
Title: General Manager
Date Signed: _____

By: _____
Print name: Brian Osborn
Title: _____
Date Signed: _____

Engineer License or Firm's Certificate No. (if required):

State of: Nebraska

Address for Owner's receipt of notices:
P-MRNRD

8901 S. 154th Street
Omaha, NE 68138-3621

Designated Representative (Paragraph 8.03.A):
Martin Cleveland
Title: Construction Engineer
Phone Number: 402-315-1707
E-Mail Address: mcleveland@papiionrd.org

Address for Engineer's receipt of notices:

601 P Street
Suite 200
Lincoln, NE 68508

Designated Representative (Paragraph 8.03.A):
Daniel Lightbody, P.E.
Title: Project Manager
Phone Number: 402-458-5003
E-Mail Address: dlightbody@olsson.com

This document is a MODIFIED VERSION of

This is **EXHIBIT A**, consisting of 17 pages, referred to in and part of the **Agreement between Owner and Engineer for Professional Services** dated September 10, 2021.

Engineer's Scope of Services

Article 1 of the Agreement is supplemented to include the following agreement of the parties.

Engineer shall provide the Basic Services identified in Attachment 1 to Exhibit A (Proposed Scope of Services), and Attachment 2 to Exhibit A (Time Schedule Chart) pursuant to the terms set forth in Part 1 of Exhibit A below. Engineer shall provide Additional Services, if necessary, pursuant to the terms set forth in Part 2 of Exhibit A below. In the event that there is a conflict regarding the Scope of Services to be performed, Attachment 1 of Exhibit A shall prevail.

PART 1 – BASIC SERVICES

A1.01 Study and Report Phase

A. Engineer shall:

1. Consult with Owner to define and clarify Owner's requirements for the Project, including design objectives and constraints, space, capacity and performance requirements, flexibility, and expandability, and any budgetary limitations, and identify available data, information, reports, facilities plans, and site evaluations.
 - a. If Owner has already identified one or more potential solutions to meet its Project requirements, then proceed with the study and evaluation of such potential solutions:

A site investigation will be performed as detailed in attached Scope and a maximum of two repair alternatives will be presented for consideration.
 - b. If Owner has not identified specific potential solutions for study and evaluation, then assist Owner in determining whether Owner's requirements, and available data, reports, plans, and evaluations, point to a single potential solution for Engineer's study and evaluation, or are such that it will be necessary for Engineer to identify, study, and evaluate multiple potential solutions.
 - c. If it is necessary for Engineer to identify, study, and evaluate multiple potential solutions, then identify two (2) alternative solutions potentially available to Owner, unless Owner and Engineer mutually agree that some other specific number of alternatives should be identified, studied, and evaluated.
2. Identify potential solution(s) to meet Owner's Project requirements, as needed.
3. Study and evaluate the potential solution(s) to meet Owner's Project requirements.

MODIFIED VERSION of

Exhibit A – Engineer's Services

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

4. Visit the Site, or potential Project sites, to review existing conditions and facilities, unless such visits are not necessary or applicable to meeting the objectives of the Study and Report Phase.
5. Advise Owner of any need for Owner to obtain, furnish, or otherwise make available to Engineer additional Project-related data and information, for Engineer's use in the study and evaluation of potential solution(s) to Owner's Project requirements, and preparation of a related report.
6. After consultation with Owner, recommend to Owner the solution(s) which in Engineer's judgment meet Owner's requirements for the Project.
7. Identify, consult with, and analyze requirements of governmental authorities having jurisdiction to approve the portions of the Project to be designed or specified by Engineer, including but not limited to mitigating measures identified in an environmental assessment for the Project.
8. Prepare a report (the "Report") which will, as appropriate, contain schematic layouts, sketches, and conceptual design criteria with appropriate exhibits to indicate the agreed-to requirements, considerations involved, and Engineer's recommended solution(s). For each recommended solution Engineer will provide the following, which will be separately itemized: opinion of probable Construction Cost; proposed allowances for contingencies; the estimated total costs of design, professional, and related services to be provided by Engineer and its Consultants; and, on the basis of information furnished by Owner, a tabulation of other items and services included within the definition of Total Project Costs.
9. Advise Owner of any need for Owner to provide data or services of the types described in Exhibit B, for use in Project design, or in preparation for Contractor selection and construction.
10. If requested to do so by Owner, assist Owner in evaluating the possible use of building information modeling; civil integrated management; geotechnical baselining of subsurface site conditions; innovative design, contracting, or procurement strategies; or other strategies, technologies, or techniques for assisting in the design, construction, and operation of Owner's facilities. The subject matter of this paragraph shall be referred to in Exhibit A and B as "Project Strategies, Technologies, and Techniques."
11. If requested to do so by Owner, assist Owner in identifying opportunities for enhancing the sustainability of the Project, and pursuant to Owner's instructions plan for the inclusion of sustainable features in the design.
12. Use ASCE 38, "Standard Guideline for the Collection and Depiction of Existing Subsurface Utility Data" as a means to advise the Owner on a recommended scope of work and procedure for the identification and mapping of existing utilities.

MODIFIED VERSION of

Exhibit A – Engineer's Services

13. Develop a scope of work and survey limits for any topographic and other surveys necessary for design.
 14. Perform or provide the following other Study and Report Phase tasks or deliverables: Deliverables, based upon phases chosen to perform, can include the following: Topo survey results, description of preliminary findings, and wetland delineation survey.
 15. Furnish 2 review copies of the Report and any other Study and Report Phase deliverables to Owner within 14 calendar days of the Effective Date and review it with Owner. Within 14 calendar days of Engineer's review with Owner, Owner shall submit to Engineer any comments regarding the furnished items.
 16. Revise the Report and any other Study and Report Phase deliverables in response to Owner's comments, as appropriate, and furnish 2 copies of the revised Report and any other Study and Report Phase deliverables to the Owner within 14 calendar days of receipt of Owner's comments.
- B. Engineer's services under the Study and Report Phase will be considered complete on the date when Engineer has delivered to Owner the revised Report and any other Study and Report Phase deliverables and Owner has confirmed that Owner has confirmed in writing that it has no additional comments to the Report or any other Study and Report Phase deliverable.

A1.02 Preliminary Design Phase

- A. After acceptance by Owner of the Report and any other Study and Report Phase deliverables; selection by Owner of a recommended solution; issuance by Owner of any instructions of for use of Project Strategies, Technologies, and Techniques, or for inclusion of sustainable features in the design; and indication by Owner of any specific modifications or changes in the scope, extent, character, or design requirements of the Project desired by Owner, and upon written authorization from Owner, Engineer shall:
1. Prepare Preliminary Design Phase documents consisting of final design criteria, preliminary drawings, outline specifications, and written descriptions of the Project.
 2. In preparing the Preliminary Design Phase documents, use any specific applicable Project Strategies, Technologies, and Techniques authorized by Owner during or following the Study and Report Phase, and include sustainable features, as appropriate, pursuant to Owner's instructions.
 3. Provide necessary field surveys and topographic and utility mapping for Engineer's design purposes. Comply with the scope of work and procedure for the identification and mapping of existing utilities selected and authorized by Owner pursuant to advice from Engineer based on ASCE 38, "Standard Guideline for the Collection and Depiction of Existing Subsurface Utility Data," as set forth in Paragraph A1.01.A.12 above. If no such scope of work and procedure for utility mapping has been selected and authorized,

MODIFIED VERSION of

Exhibit A – Engineer's Services

then at a minimum the utility mapping will include Engineer contacting utility owners and obtaining all available information.

4. Visit the Site as needed to prepare the Preliminary Design Phase documents.
 5. Advise Owner if additional reports, data, information, or services of the types described in Exhibit B are necessary and assist Owner in obtaining such reports, data, information, or services.
 6. Continue to assist Owner with Project Strategies, Technologies, and Techniques that Owner has chosen to implement.
 7. Based on the information contained in the Preliminary Design Phase documents, prepare a revised opinion of probable Construction Cost, and assist Owner in tabulating the various cost categories which comprise Total Project Costs.
 8. Obtain and review the Owner Requirements and Owner's instructions regarding Owner's procurement of construction services (including instructions regarding advertisements for bids, instructions to bidders, and requests for proposals, as applicable), Owner's construction contract practices and requirements, insurance and bonding requirements, electronic transmittals during construction, and other information necessary for the finalization of Owner's bidding-related documents (or requests for proposals or other construction procurement documents), and Construction Contract Documents. Also obtain and review copies of Owner's design and construction standards, Owner's standard forms, general conditions (if other than EJCDC® C-700, Standard General Conditions of the Construction Contract, 2013 Edition), supplementary conditions, text, and related documents or content for Engineer to include in the draft bidding-related documents (or requests for proposals or other construction procurement documents), and in the draft Construction Contract Documents, when applicable.
 9. Perform or provide the following other Preliminary Design Phase tasks or deliverables:

Deliverables include: 30% design plans and a progress meeting to discuss project feasibility and status.
 10. Furnish 2 review copies of the Preliminary Design Phase documents, opinion of probable Construction Cost, and any other Preliminary Design Phase deliverables to Owner and review them with Owner. Owner shall submit to Engineer any comments regarding the furnished items.
 11. Revise the Preliminary Design Phase documents, opinion of probable Construction Cost, and any other Preliminary Design Phase deliverables in response to Owner's comments, as appropriate, and furnish to Owner 2 copies of the revised Preliminary Design Phase documents, revised opinion of probable Construction Cost, and any other deliverables within 14 calendar days after receipt of Owner's comments.
- B. Engineer's services under the Preliminary Design Phase will be considered complete on the date when Engineer has delivered to Owner the revised Preliminary Design Phase

MODIFIED VERSION of

Exhibit A – Engineer's Services

documents, revised opinion of probable Construction Cost, and any other Preliminary Design Phase deliverables and Owner has confirmed in writing that Owner has no additional comments to such documents and/or deliverables.

A1.03 *Final Design Phase*

- A. After acceptance by Owner of the Preliminary Design Phase documents, revised opinion of probable Construction Cost as determined in the Preliminary Design Phase, and any other Preliminary Design Phase deliverables, subject to any Owner-directed modifications or changes in the scope, extent, character, or design requirements of or for the Project, and upon written authorization from Owner, Engineer shall:
1. Prepare final Drawings and Specifications indicating the scope, extent, and character of the Work to be performed and furnished by Contractor.
 2. Visit the Site as needed to assist in preparing the final Drawings and Specifications.
 3. Provide technical criteria, written descriptions, and design data for Owner's use in filing applications for permits from or approvals of governmental authorities having jurisdiction to review or approve the final design; assist Owner in consultations with such authorities; and revise the Drawings and Specifications in response to directives from such authorities, as appropriate.
 4. Advise Owner of any recommended adjustments to the opinion of probable Construction Cost.
 5. After consultation with Owner, include in the Construction Contract Documents any specific protocols for the transmittal of Project-related correspondence, documents, text, data, drawings, information, and graphics, in electronic media or digital format, either directly, or through access to a secure Project website. Any such protocols shall be applicable to transmittals between and among Owner, Engineer, and Contractor during the Construction Phase and Post-Construction Phase, and unless agreed otherwise shall supersede any conflicting protocols previously established for transmittals between Owner and Engineer.
 6. Assist Owner in assembling known reports and drawings of Site conditions, and in identifying the technical data contained in such reports and drawings upon which bidders or other prospective contractors may rely.
 7. In addition to preparing the final Drawings and Specifications, assemble drafts of other Construction Contract Documents based on specific instructions and contract forms, text, or content received from Owner.
 8. If requested by Owner, prepare or assemble draft bidding-related documents (or requests for proposals or other construction procurement documents), based on the specific bidding or procurement-related instructions and forms, text, or content received from Owner.

MODIFIED VERSION of

Exhibit A – Engineer's Services

9. Perform or provide the following other Final Design Phase tasks or deliverables:

Deliverables, based upon phases chosen to perform, can include the following: 404 Wetland Permit, final construction plans, or final construction specifications.

10. Furnish for review by Owner, its legal counsel, and other advisors, 2 copies of the final Drawings and Specifications, assembled drafts of other Construction Contract Documents, the draft bidding-related documents (or requests for proposals or other construction procurement documents), and any other Final Design Phase deliverables, within 7 calendar days of authorization to proceed with the Final Design Phase, and review them with Owner. Owner shall submit to Engineer any comments regarding the furnished items, and any instructions for revisions.
11. Revise the final Drawings and Specifications, assembled drafts of other Construction Contract Documents, the draft bidding-related documents (or requests for proposals or other construction procurement documents), and any other Final Design Phase deliverables in accordance with comments and instructions from the Owner, as appropriate, and submit 2 final copies of such documents to Owner within 7 calendar days after receipt of Owner's comments and instructions.
- B. Engineer's services under the Final Design Phase will be considered complete on the date when Engineer has delivered to Owner the final Drawings and Specifications, other assembled Construction Contract Documents, bidding-related documents (or requests for proposals or other construction procurement documents), and any other Final Design Phase deliverables, and Owner has provided Engineer with written confirmation that Owner has no additional comments to any of the foregoing items.
- C. In the event that the Work designed or specified by Engineer is to be performed or furnished under more than one prime contract, or if Engineer's services are to be separately sequenced with the work of one or more prime Contractors (such as in the case of fast-tracking), Owner and Engineer shall, prior to commencement of the Final Design Phase, develop a schedule for performance of Engineer's services during the Final Design, Bidding or Negotiating, Construction, and Post-Construction Phases in order to sequence and coordinate properly such services as are applicable to the work under such separate prime contracts. This schedule is to be prepared and included in or become an amendment to Exhibit A whether or not the work under such contracts is to proceed concurrently.
- D. The number of prime contracts for Work designed or specified by Engineer upon which the Engineer's compensation has been established under this Agreement is 1. If more prime contracts are awarded, Engineer shall be entitled to an equitable increase in its compensation under this Agreement.

A1.04 Bidding or Negotiating Phase

- A. After acceptance by Owner of the final Drawings and Specifications, other Construction Contract Documents, bidding-related documents (or requests for proposals or other construction procurement documents), and the most recent opinion of probable

MODIFIED VERSION of

Exhibit A – Engineer's Services

Construction Cost as determined in the Final Design Phase, and upon written authorization by Owner to proceed, Engineer shall:

1. Assist Owner in advertising for and obtaining bids or proposals for the Work, assist Owner in issuing assembled design, contract, and bidding-related documents (or requests for proposals or other construction procurement documents) to prospective contractors, and, where applicable, maintain a record of prospective contractors to which documents have been issued, attend pre-bid conferences, if any, and receive and process contractor deposits or charges for the issued documents.
2. Prepare and issue Addenda as appropriate to clarify, correct, or change the issued documents.
3. Provide information or assistance needed by Owner in the course of any review of proposals or negotiations with prospective contractors.
4. Consult with Owner as to the qualifications of prospective contractors.
5. Consult with Owner as to the qualifications of subcontractors, suppliers, and other individuals and entities proposed by prospective contractors, for those portions of the Work as to which review of qualifications is required by the issued documents.
6. If the issued documents require, the Engineer shall evaluate and determine the acceptability of "or equals" and substitute materials and equipment proposed by prospective contractors, provided that such proposals are allowed by the bidding-related documents (or requests for proposals or other construction procurement documents) prior to award of contracts for the Work. Services under this paragraph are subject to the provisions of Paragraph A2.02.A.2 of this Exhibit A.
7. Attend the bid opening, prepare bid tabulation sheets to meet Owner's schedule, and assist Owner in evaluating bids or proposals, assembling final contracts for the Work for execution by Owner and Contractor, and in issuing notices of award of such contracts.
8. If Owner engages in negotiations with bidders or proposers, assist Owner with respect to technical and engineering issues that arise during the negotiations.
9. Perform or provide the following other Bidding or Negotiating Phase tasks or deliverables:

Phase will be considered complete when the executed construction contracts have been approved by the Project Sponsor. Re-advertising, if necessary, will be negotiated under an amendment to this Agreement.

- B. The Bidding or Negotiating Phase will be considered complete upon commencement of the Construction Phase or upon cessation of negotiations with prospective contractors (except as may be required if Exhibit F is a part of this Agreement).

MODIFIED VERSION of

Exhibit A – Engineer's Services

A1.05 Construction Phase

- A. Upon successful completion of the Bidding and Negotiating Phase, and upon written authorization from Owner, Engineer shall:
1. *General Administration of Construction Contract:* Consult with Owner and act as Owner's representative as provided in the Construction Contract. The extent and limitations of the duties, responsibilities, and authority of Engineer shall be as assigned in the Standard General Conditions or other construction general conditions specified in this Agreement. The duties, responsibilities, and authority of Engineer in the Construction Contract may be modified only with the Engineer's consent. Engineer shall not be required to furnish or perform services contrary to Engineer's responsibilities as a licensed professional. All of Owner's instructions to Contractor will be issued through Engineer, which shall have authority to act on behalf of Owner in dealings with Contractor to the extent provided in this Agreement and the Construction Contract except as otherwise provided in writing.
 2. *Resident Project Representative (RPR):* Provide the services of an RPR at the Site to assist the Engineer and to provide more extensive observation of Contractor's work. Duties, responsibilities, and authority of the RPR are as set forth in Exhibit D. The furnishing of such RPR's services will not limit, extend, or modify Engineer's responsibilities or authority except as expressly set forth in Exhibit D. RPR Services are not included. However, they can be added at any time if deemed necessary under an amendment to this Agreement on a time and expense basis per the attached Labor Rate Schedule.
 3. *Selection of Independent Testing Laboratory:* Assist Owner in the selection of an independent testing laboratory to perform the services identified in Exhibit B, Paragraph B2.01.
 4. *Pre-Construction Conference:* Participate in a pre-construction conference prior to commencement of Work at the Site.
 5. *Electronic Transmittal Protocols:* If the Construction Contract Documents do not specify protocols for the transmittal of Project-related correspondence, documents, text, data, drawings, information, and graphics, in electronic media or digital format, either directly, or through access to a secure Project website, then together with Owner and Contractor jointly develop such protocols for transmittals between and among Owner, Contractor, and Engineer during the Construction Phase and Post-Construction Phase.
 6. *Original Documents:* If requested by Owner to do so, maintain and safeguard during the Construction Phase at least one original printed record version of the Construction Contract Documents, including Drawings and Specifications signed and sealed by Engineer and other design professionals in accordance with applicable Laws and Regulations. Throughout the Construction Phase, upon request, make such original printed record version of the Construction Contract Documents available to Contractor and Owner for review.

MODIFIED VERSION of

Exhibit A – Engineer's Services

7. *Schedules:* Receive, review, and determine the acceptability of any and all schedules that Contractor is required to submit to Engineer, including the Progress Schedule, Schedule of Submittals, and Schedule of Values.
8. *Baselines and Benchmarks:* As appropriate, establish baselines and benchmarks for locating the Work which in Engineer's judgment are necessary to enable Contractor to proceed.
9. *Visits to Site and Observation of Construction:* In connection with observations of Contractor's Work while it is in progress:
 - a. Make visits to the Site at intervals appropriate to the various stages of construction, as Engineer deems necessary and/or as reasonably requested by Owner, to observe as an experienced and qualified design professional the progress of Contractor's executed Work. Such visits and observations by Engineer, and the Resident Project Representative, if any, are not intended to be exhaustive or to extend to every aspect of the Work or to involve detailed inspections of the Work beyond the responsibilities specifically assigned to Engineer in this Agreement and the Construction Contract Documents, but rather are to be limited to spot checking, selective sampling, and similar methods of general observation of the Work based on Engineer's exercise of professional judgment, as assisted by the Resident Project Representative, if any. Based on information obtained during such visits and observations, Engineer will determine in general if the Work is proceeding in accordance with the Construction Contract Documents, and Engineer shall keep Owner informed of the progress of the Work.
 - b. The purpose of Engineer's visits to the Site, and representation by the Resident Project Representative, if any, at the Site, will be to enable Engineer to better carry out the duties and responsibilities assigned to and undertaken by Engineer during the Construction Phase, and, in addition, by the exercise of Engineer's efforts as an experienced and qualified design professional, to provide for Owner confidence that the completed Work will conform in general to the Construction Contract Documents and that Contractor has implemented and maintained the integrity of the design concept of the completed Project as a functioning whole as indicated in the Construction Contract Documents. Engineer shall not on its own behalf with respect to third parties, during such visits or as a result of such observations of the Work, be deemed to supervise, direct, or have control over the Work, nor shall Engineer have authority over or responsibility for the means, methods, techniques, sequences, or procedures of construction selected or used by any Constructor, for security or safety at the Site, for safety precautions and programs incident to any Constructor's work in progress, for the coordination of the Constructors' work or schedules, nor for any failure of any Constructor to comply with Laws and Regulations applicable to furnishing and performing of its work. Accordingly, Engineer neither guarantees the performance of any Constructor nor assumes responsibility for any Constructor's failure to furnish or perform the Work, or any portion of the Work, in accordance with the Construction Contract Documents

MODIFIED VERSION of

Exhibit A – Engineer's Services

unless such failure is caused in whole or in part by Engineer, its Consultants, agents or other representatives.

10. *Defective Work:* Reject Work if Engineer believes that such Work is defective under the terms and standards set forth in the Construction Contract Documents, that such Work will not produce a completed Project that conforms generally to the Construction Contract Documents and/or that it will threaten the integrity of the design concept of the completed Project as a functioning whole as indicated in the Construction Contract Documents. Provide recommendations to Owner regarding whether Contractor should correct such Work or remove and replace such Work, or whether Owner should consider accepting such Work as provided in the Construction Contract Documents.
11. *Compatibility with Design Concept:* If Engineer believes that a specific part of the Work that is not defective under the terms and standards set forth in the Construction Contract Documents is nonetheless not compatible with the design concept of the completed Project as a functioning whole, then inform Owner of such incompatibility, and provide recommendations for addressing such Work.
12. *Clarifications and Interpretations:* Accept from Contractor and Owner submittal of all matters in question concerning the requirements of the Construction Contract Documents (sometimes referred to as requests for information or interpretation—RFIs), or relating to the acceptability of the Work under the Construction Contract Documents. Promptly to ensure the orderly completion of Contractor's work, render a written clarification, interpretation, or decision on the issue submitted, or initiate an amendment or supplement to the Construction Contract Documents. Such clarifications, interpretations and/or decisions must be consistent with the intent and reasonably inferable from the Construction Contract Documents.
13. *Intentionally Deleted.*
14. *Field Orders:* Subject to any limitations in the Construction Contract Documents, Engineer may prepare and issue Field Orders requiring minor changes in the Work. Engineer shall promptly notify Owner of any issued Field Order.
15. *Change Orders and Work Change Directives:* Recommend Change Orders and Work Change Directives to Owner, as appropriate, and prepare Change Orders and Work Change Directives as required.
16. *Differing Site Conditions:* Respond to any notice from Contractor of differing site conditions, including conditions relating to underground facilities such as utilities, and hazardous environmental conditions. Promptly conduct reviews and prepare findings, conclusions, and recommendations for Owner's use.
17. *Shop Drawings, Samples, and Other Submittals:* Review and approve or take other appropriate action with respect to Shop Drawings, Samples, and other required Contractor submittals, but only for conformance with the information given in the Construction Contract Documents and compatibility with the design concept of the

MODIFIED VERSION of

Exhibit A – Engineer's Services

completed Project as a functioning whole as indicated by the Construction Contract Documents. Such reviews and approvals or other action will not extend to means, methods, techniques, sequences, or procedures of construction or to safety precautions and programs incident thereto. Engineer shall meet any Contractor's submittal schedule that Engineer has accepted.

18. *Substitutes and "Or-equal"*: Evaluate and determine the acceptability of substitute or "or-equal" materials and equipment proposed by Contractor, but subject to the provisions of Paragraph A2.02.A.2 of this Exhibit A.
19. *Inspections and Tests*:
 - a. Require such special inspections and/or tests of Contractor's work as deemed reasonably necessary, and receive and review all certificates of inspections, tests, and approvals required by Laws and Regulations or the Construction Contract Documents. Engineer's review of such certificates will be for the purpose of determining that the results certified indicate compliance with the Construction Contract Documents and will not constitute an independent evaluation that the content or procedures of such inspections, tests, or approvals comply with the requirements of the Construction Contract Documents. Engineer shall be entitled to rely on the results of such inspections and tests.
 - b. As deemed reasonably necessary, request that Contractor uncover Work that is to be inspected, tested, or approved.
 - c. Pursuant to the terms of the Construction Contract, require special inspections or testing of the Work, whether or not the Work is fabricated, installed, or completed.
20. *Change Proposals and Claims*: (a) Review and respond to Change Proposals. Review each duly submitted Change Proposal from Contractor and, within 30 calendar days after receipt of the Contractor's supporting data, either deny the Change Proposal in whole, approve it in whole, or deny it in part and approve it in part. Such actions shall be in writing, with a copy provided promptly to Owner and Contractor. (b) Provide information or data to Owner regarding engineering or technical matters pertaining to Claims.
21. *Applications for Payment*: Based on Engineer's observations as an experienced and qualified design professional and on review of Applications for Payment and accompanying supporting documentation:
 - a. Determine the amounts that Engineer recommends Contractor be paid. Recommend reductions in payment (set-offs) based on the provisions for set-offs stated in the Construction Contract. Such recommendations of payment and reductions in payment will be in writing and will constitute Engineer's representation to Owner, that, to the best of Engineer's knowledge, information and belief, taking into account its observations and review and such other information available to Engineer, Contractor's Work has progressed to the point

MODIFIED VERSION of

Exhibit A – Engineer's Services

indicated, the Work is generally in accordance with the Construction Contract Documents (subject to an evaluation of the Work as a functioning whole prior to or upon Substantial Completion, to the results of any subsequent tests called for in the Construction Contract Documents, and to any other qualifications stated in the recommendation), and the conditions precedent to Contractor's being entitled to such payment appear to have been fulfilled in so far as it is Engineer's responsibility to observe the Work. In the case of unit price Work, Engineer's recommendations of payment will include final determinations of quantities and classifications of the Work (subject to any subsequent adjustments allowed by the Construction Contract Documents).

- b. By recommending payment, Engineer shall not thereby be deemed to have represented those observations made by Engineer to check the quality or quantity of Contractor's Work as it is performed and furnished have been exhaustive, extended to every aspect of Contractor's Work in progress, or involved detailed inspections of the Work beyond the responsibilities specifically assigned to Engineer in this Agreement. Neither Engineer's review of Contractor's Work for the purposes of recommending payments nor Engineer's recommendation of any payment including final payment will impose on Engineer responsibility to supervise, direct, or control the Work, or for the means, methods, techniques, sequences, or procedures of construction or safety precautions or programs incident thereto, or Contractor's compliance with Laws and Regulations applicable to Contractor's furnishing and performing the Work. It will also not impose responsibility on Engineer to make any examination to ascertain how or for what purposes Contractor has used the money paid to Contractor by Owner; to determine that title to any portion of the Work, including materials or equipment, has passed to Owner free and clear of any liens, claims, security interests, or encumbrances; or that there may not be other matters at issue between Owner and Contractor that might affect the amount that should be paid.
22. *Contractor's Completion Documents:* Receive from Contractor, review, and transmit to Owner maintenance and operating instructions, schedules, guarantees, bonds, certificates or other evidence of insurance required by the Construction Contract Documents, certificates of inspection, tests and approvals, and Shop Drawings, Samples, and other data approved as provided under Paragraph A1.05.A.17. Receive from Contractor, review, and transmit to Owner the annotated record documents which are to be assembled by Contractor in accordance with the Construction Contract Documents to obtain final payment. The extent of Engineer's review of record documents shall be as provided in Paragraph A1.05.A.17 and to check that Contractor has submitted all pages.
 23. *Substantial Completion:* Promptly after notice from Contractor that Contractor considers the entire Work ready for its intended use, in company with Owner and Contractor, visit the Site to conduct review and conduct an inspection of the Work to determine the status of completion. Follow the procedures in the Construction Contract regarding the preliminary certificate of Substantial Completion, punch list of items to be completed, Owner's objections, notice to Contractor, and issuance of a final certificate

MODIFIED VERSION of

Exhibit A – Engineer's Services

of Substantial Completion. Assist Owner regarding any remaining engineering or technical matters affecting Owner's use or occupancy of the Work following Substantial Completion.

24. *Other Tasks:* Perform or provide the following other Construction Phase tasks or deliverables: N/A
 25. *Final Notice of Acceptability of the Work:* Conduct a final inspection to determine if the Work is complete and acceptable so that Engineer may recommend, in writing, final payment to Contractor. Accompanying the recommendation for final payment, Engineer shall also provide a notice to Owner and Contractor in the form attached hereto as Exhibit E ("Notice of Acceptability of Work") that the Work is acceptable (subject to the provisions of the Notice and Paragraph A1.05.A.21.b) to the best of Engineer's knowledge, information, and belief, and based on the extent of the services provided by Engineer under this Agreement.
 26. *Standards for Certain Construction-Phase Decisions:* Engineer will render decisions regarding the requirements of the Construction Contract Documents, and judge the acceptability of the Work, pursuant to the specific procedures set forth in the Construction Contract for initial interpretations, Change Proposals, and acceptance of the Work. In rendering such decisions and judgments, Engineer will not show partiality to Owner or Contractor, and will not be liable to Owner, Contractor, or others in connection with any proceedings, interpretations, decisions, or judgments to the extent conducted or rendered in good faith.
- B. *Duration of Construction Phase:* The Construction Phase will commence with the execution of the first Construction Contract for the Project or any part thereof and will terminate upon written recommendation by Engineer for final payment to Contractors. If the Project involves more than one prime contract as indicated in Paragraph A1.03.D, then Construction Phase services may be rendered at different times in respect to the separate contracts. Subject to the provisions of Article 3, Engineer shall be entitled to an equitable increase in compensation if Construction Phase services (including Resident Project Representative services, if any) are required after the original date for completion and readiness for final payment of Contractor as set forth in the Construction Contract.

A1.06 *Post-Construction Phase*

- A. Upon written authorization from Owner during the Post-Construction Phase, Engineer shall:
1. Together with Owner, visit the Project to observe any apparent defects in the Work, make recommendations as to replacement or correction of defective Work, if any, or the need to repair of any damage to the Site or adjacent areas, and assist Owner in consultations and discussions with Contractor concerning correction of any such defective Work and any needed repairs.

MODIFIED VERSION of

Exhibit A – Engineer's Services

2. Together with Owner, visit the Project within one month before the end of the Construction Contract's correction period to ascertain whether any portion of the Work or the repair of any damage to the Site or adjacent areas is defective and therefore subject to correction by Contractor.
 3. Provide assistance in connection with the adjusting of Project equipment and systems.
 4. Assist Owner in training Owner's staff to operate and maintain Project equipment and systems.
 5. Assist Owner in developing procedures for control of the operation and maintenance of, and record keeping for Project equipment and systems.
 6. Perform or provide the following other Post-Construction Phase tasks or deliverables:
N/A
- B. The Post-Construction Phase services may commence during the Construction Phase and, if not otherwise modified in this Exhibit A, will terminate twelve months after the commencement of the Construction Contract's correction period.

PART 2 – ADDITIONAL SERVICES

A2.01 *Additional Services Requiring Owner's Written Authorization*

- C. If authorized in writing by Owner, Engineer shall provide Additional Services of the types listed below. These services are not included as part of Basic Services and will be paid for by Owner as indicated in Exhibit C.
1. Preparation of applications and supporting documents (in addition to those furnished under Basic Services) for private or governmental grants, loans, or advances in connection with the Project; preparation or review of environmental assessments and impact statements; review and evaluation of the effects on the design requirements for the Project of any such statements and documents prepared by others; and assistance in obtaining approvals of authorities having jurisdiction over the anticipated environmental impact of the Project.
 2. Services to make measured drawings of existing conditions or facilities, to conduct tests or investigations of existing conditions or facilities, or to verify the accuracy of drawings or other information furnished by Owner or others.
 3. Services resulting from significant changes in the scope, extent, or character of the portions of the Project designed or specified by Engineer, or the Project's design requirements, including, but not limited to, changes in size, complexity, Owner's schedule, character of construction, or method of financing; and revising previously accepted studies, reports, Drawings, Specifications, or Construction Contract Documents when such revisions are required by changes in Laws and Regulations enacted subsequent to the Effective Date or are due to any other causes beyond Engineer's control.

MODIFIED VERSION of

Exhibit A – Engineer's Services

4. Services resulting from Owner's request to evaluate additional Study and Report Phase alternative solutions beyond those agreed to in Paragraph A1.01.A.1 and 2.
5. Services required as a result of Owner's providing incomplete or incorrect Project information to Engineer.
6. Providing renderings or models for Owner's use, including services in support of building information modeling or civil integrated management.
7. Undertaking investigations and studies including, but not limited to:
 - a. detailed consideration of operations, maintenance, and overhead expenses;
 - b. the preparation of feasibility studies (such as those that include projections of output capacity, utility project rates, project market demand, or project revenues) and cash flow analyses, provided that such services are based on the engineering and technical aspects of the Project, and do not include rendering advice regarding municipal financial products or the issuance of municipal securities;
 - c. preparation of appraisals;
 - d. evaluating processes available for licensing, and assisting Owner in obtaining process licensing;
 - e. detailed quantity surveys of materials, equipment, and labor; and
 - f. audits or inventories required in connection with construction performed or furnished by Owner.
8. Furnishing services of Consultants for other than Basic Services.
9. Providing data or services of the types described in Exhibit B, when Owner retains Engineer to provide such data or services instead of Owner furnishing the same.
10. Providing the following services:
 - a. Services attributable to more prime construction contracts than specified in Paragraph A1.03.D.
 - b. Services to arrange for performance of construction services for Owner by contractors other than the principal prime Contractor, and administering Owner's contract for such services.
11. Services during out-of-town travel required of Engineer, other than for visits to the Site or Owner's office as required in Basic Services (Part 1 of Exhibit A).
12. Preparing for, coordinating with, participating in and responding to structured independent review processes, including, but not limited to, construction management,

MODIFIED VERSION of

Exhibit A – Engineer's Services

cost estimating, project peer review, value engineering, and constructability review requested by Owner in writing; and performing or furnishing services required to revise studies, reports, Drawings, Specifications, or other documents as a result of such review processes.

13. Preparing additional bidding-related documents (or requests for proposals or other construction procurement documents) or Construction Contract Documents for alternate bids or cost estimates requested by Owner for the Work or a portion thereof.
14. Assistance in connection with bid protests, rebidding, or renegotiating contracts for construction, materials, equipment, or services, except when such assistance is required to complete services required by Paragraph 5.02.A and Exhibit F.
15. *Intentionally deleted.*
16. Providing Construction Phase services beyond the original date for completion and readiness for final payment of Contractor, but only if and to the extent such services increase the total quantity of services to be performed in the Construction Phase, rather than merely shifting performance of such services to a later date.
17. Preparing Record Drawings, and furnishing such Record Drawings to Owner.
18. Supplementing Record Drawings with information regarding the completed Project, Site, and immediately adjacent areas obtained from field observations, Owner, utility companies, and other reliable sources.
19. Conducting surveys, investigations, and field measurements to verify the accuracy of Record Drawing content obtained from Contractor, Owner, utility companies, and other sources; revise and supplement Record Drawings as needed.
20. Preparation of operation, maintenance, and staffing manuals.
21. *Intentionally Deleted.*
22. *Intentionally Deleted.*
23. *Intentionally Deleted.*
24. Preparing to serve or serving as a consultant or witness for Owner in any litigation, arbitration, lien or bond claim, or other legal or administrative proceeding or dispute related to the Project.
25. Overtime work requiring higher than regular rates.
26. Providing construction surveys and staking to enable Contractor to perform its work other than as required under Paragraph A1.05.A.8; any type of property surveys or related engineering services needed for the transfer of interests in real property; and providing other special field surveys.

MODIFIED VERSION of

Exhibit A – Engineer's Services

27. Providing more extensive services required to enable Engineer to issue notices or certifications requested by Owner.
28. *Intentionally Deleted.*
29. Other additional services performed or furnished by Engineer not otherwise provided for in this Agreement.

A2.02 Additional Services Not Requiring Owner's Written Authorization

- A. Engineer shall advise Owner in writing that Engineer is commencing to perform or furnish the Additional Services of the types listed below. For such Additional Services, Engineer need not request or obtain specific advance written authorization from Owner. Engineer shall cease performing or furnishing such Additional Services upon receipt of written notice to cease from Owner.
 1. Services in connection with Work Change Directives and Change Orders to reflect changes requested by Owner.
 2. Services in making revisions to Drawings and Specifications occasioned by the acceptance of substitute materials or equipment other than "or equal" items; services after the award of the Construction Contract in evaluating and determining the acceptability of a proposed "or equal" or substitution which is found to be inappropriate for the Project; evaluation and determination of an excessive number of proposed "or equals" or substitutions, whether proposed before or after award of the Construction Contract.
 3. Services resulting from significant delays, changes, or price increases occurring as a direct or indirect result of materials, equipment, or energy shortages.
 4. Additional or extended services during construction made necessary by (a) the presence at the Site of any Constituent of Concern or items of historical or cultural significance, (b) emergencies or acts of God endangering the Work, (c) damage to the Work by fire or other causes during construction, (d) a significant amount of defective, neglected, or delayed work by Contractor, (e) acceleration of the progress schedule involving services beyond normal working hours, or (f) default by Contractor.
 5. Services (other than Basic Services during the Post-Construction Phase) in connection with any partial utilization of the Work by Owner prior to Substantial Completion.
 6. Evaluating unreasonable or frivolous requests for interpretation or information (RFIs), Change Proposals, or other demands from Contractor or others in connection with the Work, or an excessive number of RFIs, Change Proposals, or demands.
 7. Reviewing a Shop Drawing or other Contractor submittal more than three times, as a result of repeated inadequate submissions by Contractor, except to the extent such inadequate submissions are due to Engineer, its Consultants, agents and/or other representatives.
 8. *Intentionally Deleted.*

MODIFIED VERSION of

Exhibit A – Engineer's Services

ATTACHMENT 1 TO EXHIBIT A

PROJECT DESCRIPTION AND LOCATION

Project Location: Silver Creek Watershed Sites 30 and 33, Burt County, Nebraska

Project Description:

Site 30 - Correct issue of water piping along principal spillway. Develop filter to intercept seepage and repair principal spilly & embankment.

Site 33 - Correct issue of the slope failures located on the left and right stream banks downstream of the dam.

Unless otherwise specified, tasks and phases identified in this scope will be completed at both Sites 30 and 33.

SCOPE OF SERVICES

Olsson shall provide the following services (Scope of Services) to the Client for the above-mentioned project:

PHASE 100 – Project Management

Coordination and communication with the Client, including project updates, meeting minutes, and repair alternatives.

PHASE 200 – Geotechnical Services

Task 201 – Drilling Services (Site 33 only)

1. Coordination and General Notes

- a. Olsson will contact Diggers Hotline of Nebraska to locate underground utilities. To ensure the safety of the crew on site, Olsson must also locate all private utilities and private utility service connections.
- b. Any fees resulting from the use of mud-matting or clearing operations to achieve access to boring locations is Owner's responsibility
- c. Olsson will be liable or responsible for any site disturbance that may occur as a result of bringing equipment on site.

2. Field Exploration

- a. Olsson will use a truck-mounted drill rig to complete the following soil test borings for the geotechnical exploration:
 - Two (2) soil test borings to a depth of 50 feet each; and
 - One (1) bulk sample.The soil borings will be advanced to the depths proposed, or to refusal, whichever is shallower. This scope is based on a total drilling footage of 100 linear feet.
- b. Soils will be sampled in general accordance with ASTM D1586 and ASTM D1587.
- c. Olsson will obtain groundwater levels in the test borings at the time of drilling and upon completion of the drilling operations.
- d. After obtaining groundwater level readings, Olsson will backfill the borings with bentonite chips.

MODIFIED VERSION of

Exhibit A – Engineer's Services

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

Task 202 – Geotechnical Services (Site 33 only)

1. Laboratory Services

As soil conditions dictate, laboratory testing may include visual soil classification (ASTM D2488), unconfined compression tests (ASTM D2166), thin-walled tube density tests (ASTM D7263), moisture content tests (ASTM D2216), Atterberg limit tests (ASTM D4318), Standard Proctor tests (ASTM D698), and one-dimensional consolidation tests (ASTM D2435).

2. Engineering Analysis and Report Preparation

- a. Olsson will perform engineering analyses and provide conclusions and recommendations regarding the following as per TR-60 guidelines.
- b. Analysis of the seepage observed through the north and south hillslopes, adjacent to the dam abutments.
- c. Utilize site collected survey data information provided to evaluate the global stability of the existing north and south hill slopes and possible remedial measures to stabilize the slopes. The global stability analysis with up to three cross-sections will utilize the boring and laboratory information, local experience, and engineering judgement to interpret soil properties values that can be used in a Geo/Slope W software program. A minimum safety factor of 1.5 will be required for the slope failure repair. Recommendations will be made regarding acceptable slope repair conditions based on the available soil information.
- d. Discussion of the effects of the structural fill placement on the existing soil strata.
- e. Recommendations regarding the thickness, moisture, and compaction criteria of any backfill or embankment fill.
- f. Discussion to address tractive stresses and general erosion potential of the soils.
- g. Discussion of anticipated groundwater concerns, along with recommendations for addressing these concerns during construction, if required.

Olsson's fee assumes the slope repair will consist of slope shaping and replacing the failed slope sections with a blanket drain and fill material. If more complex repair designs are needed, additional fee may be required and will be negotiated under an amendment to this agreement.

Olsson will present our conclusions and recommendations in a written report that will include a map of boring locations, soil boring logs, and a summary of laboratory tests.

PHASE 300 - Survey

At Site 33, survey data will include a topographic survey of the embankment and the failed downstream channel banks. Survey information will be used for design and layout of the proposed improvements. At Site 30, survey data collected will include top of dam elevation, auxiliary spillway elevation, and principal spillway location & elevation. Temporary hubs will be installed at both sites for use during construction.

PHASE 400 – Environmental

Wetland Delineation

Olsson will complete a Wetland Delineation of the project study area (Silver Creek 30 and 33), which is defined as approximately 0.25 acres located north of County Road J and 0.20 located north of County

MODIFIED VERSION of

Exhibit A – Engineer's Services

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

Road K in Burt County, Nebraska (See Exhibit 1). Olsson will follow the methods described in the U.S. Army Corps of Engineers (USACE) Wetland Delineation Manual (January 1987) and the Regional Supplement to the Corps of Engineers Wetland Delineation Manual: Midwest Region (Version 2.0) (March 2010).

- **Desktop Review.** The first step of the Wetland and Other Water Delineation consists of a desktop review of available databases to determine areas within the project study area that may have potential wetlands or other waters. This review will include accessing information from the National Hydrography Dataset (NHD), National Wetland Inventory (NWI), U.S. Geological Survey (USGS) 7.5-minute topographic maps, Natural Resources Conservation Service (NRCS) soil data, and current and historical aerial imagery.
- **Site Visit.** Olsson will utilize preliminary data collected from the preliminary out-of-season wetland site visit to field verify the presence or absence of wetlands and other waters identified during the preliminary out-of-season wetland site visit. The site visit must be conducted during USACE specified growing season (May 1 – October 31). The site visit will be conducted by traversing the project study area to identify wetland characteristics including hydrophytic vegetation, hydric soils, and wetland hydrology. Wetland and/or other waters boundaries will be delineated using sub-meter accuracy global positioning system (GPS) units. Midwest Region Data Forms will be filled out. Photographs documenting site conditions, including wetlands and other waters, will be taken.
- **Report.** Upon completion of the site visit a report documenting the findings of the Wetland Delineation will be prepared detailing the presence or absence of wetlands and other waters within the project study area. The Wetland Delineation Report will include a narrative of how the Wetland Delineation was conducted and a summary of the results of the Wetland Delineation. Figures documenting information gathered during the desktop review and figures showing wetland and other waters boundaries, sample point locations, and photo point locations will be included along with a photo log documenting conditions at the time of the site visit.

Section 404 Nationwide Permit Application and Coordination

- Olsson will utilize the information from the completed Wetland Delineation Report and site design information to calculate impacts to wetlands and other waters.
- Olsson assumes the project may be eligible for a Nationwide Permit (NWP) from USACE because it is believed this project will include less than 0.5 acre of impacts to jurisdictional wetlands and less than 300 linear feet of impacts to jurisdictional streams. If there are impacts to Waters of the U.S. and thus a NWP is necessary for the project, Olsson will prepare a Pre-Construction Notification (PCN) letter as part of the NWP application. As part of the NWP process, Olsson will also coordinate with the U.S. Fish and Wildlife Service (USFWS), the Nebraska Game and Parks Commission (NGPC), and the Nebraska State Historical Preservation Office (NeSHPO) as required by USACE. Should USACE request a cultural resources survey, an additional scope and fee will be required. If impacts to wetlands and waters require mitigation, additional fees and scope will be required.
- Following the submittal of the NWP application, Olsson will coordinate with USACE to verify that they have all the required information needed to process the application. Olsson assumes one (1) round of comments from USACE regarding the completeness permit application. Olsson will

MODIFIED VERSION of

Exhibit A – Engineer's Services

also coordinate with the Nebraska Department of Environment and Energy (NDEE) for circumstances where Water Quality Certification (Title 117, Nebraska Administrative Code) is required. Olsson assumes one (1) pre-application meeting with USACE at the Wherspann Field office and one (1) on-site walk-through site visit with USACE staff.

- If project changes increase impacts after the PCN submittal and a modification of the NWP application is needed, or if an Individual Permit is determined to be required after impacts have been calculated, additional fees and scope will be negotiated under an amendment to this agreement.

After the permit is obtained, a summary sheet detailing permit conditions will be prepared to assist in compliance during construction.

PHASE 500 – Design

- Olsson will provide a design plan and specifications for construction of a sand filter / seepage control and principal spillway rehabilitation / replacement based upon observed seepage path along principal spillway and pipe camera inspection performed by P-MRNRD staff. The original design plans will be used as the base for the modifications. Seepage protection & spillway rehab / replacement design plans will include the following:
 - Cover sheet showing project location (1 sheet)
 - Quantities and general project specifications (1 sheet)
 - Plan and profile of proposed seepage protection and principal spillway (1sheet)
 - Filter outlet / drainage structure details (1 sheet)
 - Project specifications outlining project details
 - Three project meetings with the NRD (Project kickoff, 60%, and 90%) for collaboration and concurrence of project scope

PHASE 600 – Plans / Project Specifications

- Olsson will develop plans and specifications for construction of the recommended slope reconstruction based upon the geotechnical report. The construction plans developed will include the following:
 - Cover sheet showing project location (1 sheet)
 - Quantities and general project specifications (1 sheet)
 - Plan and profile of proposed seepage protection and principal spillway (1sheet)
 - Filter outlet / drainage structure details (1 sheet)
 - Project specifications outlining project details
 - Engineers cost estimate
 - Three project meetings with the NRD (Project kickoff, 60%, and 90%) for collaboration and concurrence of project scope

PHASE 700 – Bidding

- Provide sufficient copies of the approved plans and specifications to the Sponsor and plan rooms for advertising and bidding. Copies of the documents to be furnished to prospective bidders at a cost fixed by Olsson.
- Mail and/or email notices to potential bidders and plan rooms. Contact contractors as needed to promote general interest in the project.

MODIFIED VERSION of

Exhibit A – Engineer's Services

- Maintain a plan holders list.
- Answer questions raised during the bidding process.
- Issue addenda as required.
- Attend the bid opening at the Sponsors location.
- Tabulate and analyze bid results.
- Review bidders' qualifications.
- Furnish a written recommendation to the Sponsor regarding the award of the construction contract. The recommendation will include:
 - a. Bid date
 - b. Summarized bid table
 - c. Evaluation of unit price extensions and total base bid. Including an error check.
 - d. Addendums and acknowledgements
 - e. Additional insured cost, if any
 - f. Confirmation of bidders signature on proposal form
 - g. Bid guarantee
 - h. Review of qualifications
 - i. Recommendation to award
 - j. Engineers cost estimate

This phase will be considered complete when the executed construction contracts have been approved by the project Sponsor. Readvertising, if necessary, will be negotiated under an amendment to this Agreement.

PHASE 800 - Construction Observation/Administration

- Conduct a pre-construction meeting. Olsson will prepare and distribute meeting minutes.
- Receive, log, and review contractor shop drawing submittals.
- Answer contractor' questions and interpret construction documents
- Olsson will provide construction observation to be performed on a per visit basis. Construction duration is estimated at 5 weeks with an average of 2 visits per week for a total of 10 visits.
- Olsson will provide post construction as-built drawings

ASSUMPTIONS

CLIENT WILL PROVIDE:

- Project Description
- Location Information
- Arranged access to the project area

ITEMS NOT INCLUDED IN SCOPE:

- NE DNR Permitting
- Bald and Golden Eagle Nest Surveys
- Threatened and Endangered Specific Survey
- Historic or Cultural Resource Surveys
- Floodplain Permitting
- Wetland Mitigation Services

MODIFIED VERSION of **Exhibit A – Engineer's Services**

This is **EXHIBIT B**, consisting of 4 pages, referred to in and part of the **Agreement between Owner and Engineer for Professional Services** dated September 10, 2021.

Owner's Responsibilities

Article 2 of the Agreement is supplemented to include the following agreement of the parties.

Silver Creek 30 and Silver Creek 33, Burt County, Nebraska

B2.01 In addition to other responsibilities of Owner as set forth in this Agreement, Owner shall at its expense:

- A. Provide Engineer with all criteria and full information as to Owner's requirements for the Project, including design objectives and constraints, space, capacity and performance requirements, flexibility, and expandability, and any budgetary limitations.
- B. Give instructions to Engineer regarding Owner's procurement of construction services (including instructions regarding advertisements for bids, instructions to bidders, and requests for proposals, as applicable), Owner's construction contract practices and requirements, insurance and bonding requirements, electronic transmittals during construction, and other information necessary for the finalization of Owner's bidding-related documents (or requests for proposals or other construction procurement documents), and Construction Contract Documents. Furnish copies (or give specific directions requesting Engineer to use copies already in Engineer's possession) of all design and construction standards, Owner's standard forms, general conditions (if other than the Standard General Conditions), supplementary conditions, text, and related documents and content for Engineer to include in the draft bidding-related documents (or requests for proposals or other construction procurement documents), and draft Construction Contract Documents, when applicable. Except to the extent Engineer makes any unauthorized Owner revisions which are not expressly acknowledged and approved by Owner in writing, Owner shall have responsibility for the final content of (1) such bidding-related documents (or requests for proposals or other construction procurement documents), and (2) those portions of any Construction Contract other than the design (as set forth in the Drawings, Specifications, or otherwise), and other engineering or technical matters; and Owner shall seek the advice of Owner's legal counsel, risk managers, and insurance advisors with respect to the drafting and content of such documents.
- C. Furnish to Engineer any other available information pertinent to the Project including reports and data relative to previous designs, construction, or investigation at or adjacent to the Site.
- D. Following Engineer's assessment of initially-available Project information and data and upon Engineer's request, furnish, or otherwise make available (if necessary through title searches, or retention of specialists or consultants) such additional Project-related information and data as is reasonably required to enable Engineer to complete its Basic and

MODIFIED VERSION of

Exhibit B – Owner's Responsibilities

Additional Services. Such additional information or data would generally include the following:

1. *Intentionally Deleted.*
 2. *Intentionally Deleted.*
 3. *Intentionally Deleted.*
 4. *Intentionally Deleted.*
 5. Explorations and tests of subsurface conditions at or adjacent to the Site; drawings of physical conditions relating to existing surface or subsurface structures at the Site; hydrographic surveys; with appropriate professional interpretation of such information or data.
 6. Environmental assessments, audits, investigations, and impact statements, and other relevant environmental, historical, or cultural studies relevant to the Project, the Site, and adjacent areas.
 7. Data or consultations as required for the Project but not otherwise identified in this Agreement.
- E. Upon Engineer's request, arrange for appropriate access to and make all provisions for Engineer to enter upon public and private property as required for Engineer to perform services under the Agreement.
- F. Recognizing and acknowledging that Engineer's services and expertise do not include the following services, provide, as required for the Project:
1. Accounting, bond and financial advisory (including, if applicable, "municipal advisor" services as described in Section 975 of the Dodd-Frank Wall Street Reform and Consumer Protection Act (2010) and the municipal advisor registration rules issued by the Securities and Exchange Commission), independent cost estimating, and insurance counseling services.
 2. Legal services with regard to issues pertaining to the Project as Owner requires, and, to the extent deemed necessary by Owner in Owner's sole discretion, that Contractor raises or Engineer reasonably requests.
 3. Such auditing services as Owner requires to ascertain how or for what purpose Contractor has used the money paid.
- G. Provide the services of an independent testing laboratory to perform all inspections, tests, and approvals of samples, materials, and equipment required by the Construction Contract Documents (other than those required to be furnished or arranged by Contractor), or to evaluate the performance of materials, equipment, and facilities of Owner, prior to their incorporation into the Work with appropriate professional interpretation thereof. Provide

MODIFIED VERSION of

Exhibit B – Owner's Responsibilities

Engineer with the findings and reports generated by testing laboratories, including findings and reports obtained from or through Contractor.

- H. Provide reviews, approvals, and permits from all governmental authorities having jurisdiction to approve all phases of the Project designed or specified by Engineer and such reviews, approvals, and consents from others as may be necessary for completion of each phase of the Project.
- I. Advise Engineer of the identity and scope of services of any independent consultants employed by Owner to perform or furnish services in regard to the Project, including, but not limited to, cost estimating, project peer review, value engineering, and constructability review.
- J. If Owner designates a construction manager or an individual or entity other than, or in addition to, Engineer to represent Owner at the Site, define and set forth as an attachment to this Exhibit B the duties, responsibilities, and limitations of authority of such other party and the relation thereof to the duties, responsibilities, and authority of Engineer.
- K. If more than one prime contract is to be awarded for the Work designed or specified by Engineer, then designate a person or entity to have authority and responsibility for coordinating the activities among the various prime Contractors, and define and set forth the duties, responsibilities, and limitations of authority of such individual or entity and the relation thereof to the duties, responsibilities, and authority of Engineer as an attachment to this Exhibit B that is to be mutually agreed upon and made a part of this Agreement before such services begin.
- L. Following Engineer's reasonable request, inform Engineer in writing of any specific requirements of safety or security programs that are applicable to Engineer, as a visitor to the Site.
- M. Examine all alternative solutions, studies, reports, sketches, Drawings, Specifications, proposals, and other documents presented by Engineer (including obtaining advice of an attorney, risk manager, insurance counselor, financial/municipal advisor, and other advisors or consultants as Owner deems appropriate in its sole discretion with respect to such examination) and render in writing decisions pertaining thereto as soon as reasonably practicable.
- N. *Intentionally Deleted.*
- O. *Intentionally Deleted.*
- P. Place and pay for advertisement for Bids in appropriate publications.
- Q. Furnish to Engineer data as to Owner's anticipated costs for services to be provided by others (including, but not limited to, accounting, bond and financial, independent cost estimating, insurance counseling, and legal advice) for Owner so that Engineer may assist Owner in collating the various cost categories which comprise Total Project Costs.

MODIFIED VERSION of

Exhibit B – Owner's Responsibilities

- R. Attend and participate in, if deemed appropriate by Owner in Owner's sole discretion, the pre-bid conference, bid opening, pre-construction conferences, construction progress and other job-related meetings, and Site visits to inspect the Work and Project to determine Substantial Completion and readiness of the completed Work for final payment.
- S. Authorize Engineer to provide Additional Services as set forth in Part 2 of Exhibit A of the Agreement, as required.
- T. Perform or provide the following: N/A

MODIFIED VERSION of

Exhibit B – Owner's Responsibilities

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

This is **EXHIBIT C**, consisting of 9 pages, referred to in and part of the **Agreement between Owner and Engineer for Professional Services** dated September 10, 2021.

Payments to Engineer for Services and Reimbursable Expenses
COMPENSATION PACKET BC-4: Basic Services – Direct Labor Costs Times a Factor

For the avoidance of doubt, this Exhibit C in its entirety is expressly subject to the last sentence of Paragraph 4.01.A in the Agreement. Article 2 of the Agreement is supplemented to include the following agreement of the parties:

ARTICLE 2 – OWNER’S RESPONSIBILITIES

C2.01 *Compensation for Basic Services (other than Resident Project Representative) – Direct Labor Costs Times a Factor Method of Payment*

A. Owner shall pay Engineer for Basic Services set forth in Exhibit A, except for services of Engineer’s Resident Project Representative, if any, as follows:

1. An amount equal to Engineer’s Direct Labor Costs times a factor of 3.15 for the services of Engineer’s personnel engaged on the Project, plus Reimbursable Expenses, estimated to be \$2,093, and Engineer’s Consultant’s charges, if any, estimated to be \$0.
2. Engineer’s Reimbursable Expenses Schedule is attached to this Exhibit C as Attachment 1.
3. The total compensation for services under Paragraph C2.01 is estimated to be \$123,603 based on the Engineer’s Fee Estimate (Time and Cost Table) attached to this Exhibit C as Attachment 2 and the following distribution of compensation:

a. Project Management	\$ 7,520
b. Study and Report Phase	\$25,256
c. Preliminary Design Phase	\$18,490
d. Final Design Phase	\$35,000
e. Bidding or Negotiating Phase	\$14,445
f. Construction Phase	\$22,892
4. Following notice to Owner, Engineer may alter the distribution of compensation between individual phases of the work noted herein to be consistent with services actually rendered. For the avoidance of doubt, in no event shall such amount, in combination with any other compensation, reimbursement and/or any other amount to be paid by Owner with respect to and/or pursuant to this Agreement exceed the

MODIFIED VERSION of

Exhibit C – Compensation Decision Guide

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

Maximum Amount unless Owner agrees otherwise in a signed written agreement entered into pursuant to this Agreement.

5. The total estimated compensation for Engineer's services included in the breakdown by phases as noted in Paragraph C2.01.A.3, incorporates all labor, overhead, profit, Reimbursable Expenses, and Engineer's Consultant's charges.
6. The portion of the amounts billed for Engineer's services which are related to services rendered on a Direct Labor Costs times a Factor basis will be billed based on the applicable Direct Labor Costs for the cumulative hours charged to the Project by Engineer's principals and employees multiplied by the above-designated factor, plus Reimbursable Expenses and Engineer's Consultant's charges reasonably and actually incurred during the billing period.
7. Direct Labor Costs means salaries and wages paid to Engineer's employees but does not include payroll-related costs or benefits.
8. The parties may, by mutual written agreement, adjust annually the Direct Labor Costs and the factor applied to Direct Labor Costs to reflect equitable changes to the compensation payable to Engineer.

C2.02 Compensation for Reimbursable Expenses

- A. Owner shall pay Engineer for all Reimbursable Expenses at the rates set forth in Appendix 1 to this Exhibit C to the extent they are actually and reasonably incurred in furtherance of the Project.
- B. Reimbursable Expenses include the expenses identified in Appendix 1 and the following: transportation (including mileage), lodging, and subsistence incidental thereto to the extent necessary for completion of the Project and specifically approved in advance by Owner in writing; providing and maintaining field office facilities including furnishings and utilities; reproduction of reports, Drawings, Specifications, bidding-related or other procurement documents, Construction Contract Documents, and similar Project-related items; and Consultants' charges. In addition, if authorized in advance by Owner, Reimbursable Expenses will also include expenses incurred for the use of highly specialized equipment.
- C. The amounts payable to Engineer for Reimbursable Expenses will be the Project-related internal expenses actually and reasonably incurred or allocated by Engineer, plus all invoiced external Reimbursable Expenses allocable to the Project, the latter multiplied by a factor of 1.0. For the avoidance of doubt, in no event will the Reimbursable Expenses, in combination with any other reimbursements, compensation and/or any other amounts to be paid by Owner with respect to and/or pursuant to this Agreement exceed the Maximum Amount unless otherwise agreed by Owner in a signed written agreement entered into pursuant to this Agreement.

C2.03 Other Provisions Concerning Payment

MODIFIED VERSION of

Exhibit C – Compensation Decision Guide

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

- A. Whenever Engineer is entitled to compensation for the charges of Engineer's Consultants, those charges shall be the amounts billed by Engineer's Consultants to Engineer times a factor of 1.0. For the avoidance of doubt, in no event will such compensation, together with any other compensation, reimbursements and/or any other amounts to be paid by Owner with respect to and/or pursuant to this Agreement exceed the Maximum Amount unless otherwise agreed by Owner in a signed written agreement entered into pursuant to this Agreement.
- B. *Factors:* The external Reimbursable Expenses and Engineer's Consultant's factors include Engineer's overhead and profit associated with Engineer's responsibility for the administration of such services and costs.

MODIFIED VERSION of

Exhibit C – Compensation Decision Guide

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

COMPENSATION PACKET RPR-4:
Resident Project Representative – Direct Labor Times a Factor

For the avoidance of doubt, this Exhibit C in its entirety is expressly subject to the last sentence of Paragraph 4.01.A in the Agreement. Article 2 of the Agreement is supplemented to include the following agreement of the parties:

C2.04 Compensation for Resident Project Representative Basic Services – Direct Labor Costs Times a Factor Method of Payment

A. Owner shall pay Engineer for:

1. ~~Resident Project Representative Services: N/A For services of Engineer's Resident Project Representative under Paragraph A1.05.A.2 of Exhibit A of the Agreement, an amount equal to Engineer's Direct Labor Costs times a factor of 3.15 for the services of Engineer's personnel engaged directly in resident Project representation, plus related Reimbursable Expenses to the extent they are actually and reasonably incurred in furtherance of the Project and Engineer's Consultant's charges to the extent they are actually and reasonably incurred in furtherance of the Project, if any. The total compensation under this paragraph is estimated to be \$1,080 per day, based upon full-time RPR services on an eight-hour workday, Monday through Friday, as requested. For the avoidance of doubt, in no event will such compensation, in combination with any other compensation, reimbursements and/or any other amounts to be paid by Owner with respect to and/or pursuant to this Agreement exceed the Maximum Amount unless otherwise agreed by Owner in a signed written agreement entered into pursuant to this Agreement. The Engineer's Fee Estimate (Time and Cost Table) is attached to this Exhibit C as Appendix 2.~~

B. Compensation for Reimbursable Expenses:

1. For those Reimbursable Expenses that are not accounted for in the compensation for Basic Services under Paragraph C2.01, and to the extent they are actually and reasonably incurred in furtherance of the Project and directly related to the provision of Resident Project Representative or Post-Construction Basic Services, Owner shall pay Engineer at the rates set forth in Appendix 1 to this Exhibit C.
2. Reimbursable Expenses include the expenses identified in Appendix 1 and the following: transportation (including mileage), lodging, and subsistence incidental thereto to the extent necessary for completion of the Project and specifically approved in advance by Owner in writing; providing and maintaining field office facilities including furnishings and utilities; reproduction of reports, Drawings, Specifications, bidding-related or other procurement documents, Construction Contract Documents, and similar Project-related items; and Consultants' charges. In addition, if authorized in advance by Owner, Reimbursable Expenses will also include expenses incurred for computer time and the use of other highly specialized equipment.

MODIFIED VERSION of

Exhibit C – Compensation Decision Guide

3. The amounts payable to Engineer for Reimbursable Expenses, if any, will be those internal expenses related to the Resident Project Representative Basic Services that are actually incurred or allocated by Engineer, plus all invoiced external Reimbursable Expenses allocable to such services, the latter multiplied by a factor of 1.0. For the avoidance of doubt, in no event will such reimbursements, in combination with any other reimbursements, compensation and/or any other amounts to be paid by Owner with respect to and/or pursuant to this Agreement exceed the Maximum Amount unless otherwise agreed by Owner in a signed written agreement entered into pursuant to this Agreement.
4. The parties may, by mutual written agreement, adjust annually the Reimbursable Expenses Schedule to reflect equitable changes in the compensation payable to Engineer.

C. Other Provisions Concerning Payment Under this Paragraph C2.04:

1. Whenever Engineer is entitled to compensation for the charges of Engineer's Consultants, those charges shall be the amounts billed by Engineer's Consultants to Engineer times a factor of 1.0. For the avoidance of doubt, in no event will such compensation, together with any other compensation, reimbursements and/or any other amounts to be paid by Owner with respect to and/or pursuant to this Agreement exceed the Maximum Amount unless otherwise agreed by Owner in a signed written agreement entered into pursuant to this Agreement.
2. *Factors:* The external Reimbursable Expenses and Engineer's Consultant's factors include Engineer's overhead and profit associated with Engineer's responsibility for the administration of such services and costs.

MODIFIED VERSION of

Exhibit C – Compensation Decision Guide

COMPENSATION PACKET AS-2:
Additional Services – Direct Labor Costs Times a Factor

Article 2 of the Agreement is supplemented to include the following agreement of the parties:

C2.05 Compensation for Additional Services – Direct Labor Costs Times a Factor Method of Payment

A. Owner shall pay Engineer for Additional Services as follows:

1. *General:* For services of Engineer's personnel engaged directly on the Project pursuant to Paragraph A2.01 or A2.02 of Exhibit A of the Agreement, except for services as a consultant or witness under Paragraph A2.01.A.24 (which if needed shall be separately negotiated based on the nature of the required consultation or testimony), an amount equal to Engineer's Direct Labor Costs times a factor of 3.15, plus related Reimbursable Expenses and Engineer's Consultant's charges, the extent they are actually and reasonably incurred in furtherance of the Project, if any.

B. *Compensation for Reimbursable Expenses:*

1. For those Reimbursable Expenses that are not accounted for in the compensation for Basic Services under Paragraph C2.01 and are actually and reasonably incurred in furtherance of the Project and directly related to the provision of Additional Services, Owner shall pay Engineer at the rates set forth in Appendix 1 to this Exhibit C.
2. Reimbursable Expenses include the expenses identified in Appendix 1 and the following: transportation (including mileage), lodging, and subsistence incidental thereto to the extent necessary for completion of the Project and specifically approved in advance by Owner in writing; providing and maintaining field office facilities including furnishings and utilities; reproduction of reports, Drawings, Specifications, bidding-related or other procurement documents, Construction Contract Documents, and similar Project-related items; and Consultants' charges. In addition, if authorized in advance by Owner, Reimbursable Expenses will also include expenses incurred for and the use of highly specialized equipment.
3. The amounts payable to Engineer for Reimbursable Expenses, if any, will be the Additional Services-related internal expenses actually incurred or allocated by Engineer, plus all invoiced external Reimbursable Expenses allocable to such Additional Services, the latter multiplied by a factor of 1.0.
4. The parties may, by mutual written agreement, adjust annually the Reimbursable Expenses Schedule to reflect equitable changes in the compensation payable to Engineer.

MODIFIED VERSION of

Exhibit C – Compensation Decision Guide

C. Other Provisions Concerning Payment for Additional Services:

1. Whenever Engineer is entitled to compensation for the charges of Engineer's Consultants, those charges shall be the amounts billed by Engineer's Consultants to Engineer times a factor of 1.0.
2. *Factors:* The external Reimbursable Expenses and Engineer's Consultant's factors include Engineer's overhead and profit associated with Engineer's responsibility for the administration of such services and costs.
3. To the extent necessary to verify Engineer's charges and upon Owner's timely request, Engineer shall make copies of such records available to Owner at cost.

MODIFIED VERSION of

Exhibit C – Compensation Decision Guide

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

This is **Attachment 1 to EXHIBIT C**, consisting of 1 page, referred to in and part of the **Agreement between Owner and Engineer for Professional Services** dated September 10, 2021.

Reimbursable Expenses Schedule

Reimbursable Expenses are subject to review and adjustment to the extent permitted by Exhibit C. Rates and charges for Reimbursable Expenses as of the date of the Agreement are:

8"x11" Copies/Impressions	\$ 0.05/page
Copies of Drawings	\$ 0.75/sq. ft.
Mileage (auto)	\$ 0.56/mile
Air Transportation	at cost
CAD Charge	\$ /hour
Laboratory Testing	at cost
Health and Safety Level D	\$ /day
Health and Safety Level C	\$ /day
Meals and Lodging	at cost

MODIFIED VERSION of

Exhibit C – Compensation Decision Guide

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

ATTACHMENT 2 TO EXHIBIT C

Place Fee Table Here

MODIFIED VERSION of

Exhibit C – Compensation Decision Guide

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

This is **EXHIBIT E**, consisting of 2 pages, referred to in and part of the **Agreement between Owner and Engineer for Professional Services** dated September 10, 2021.

NOTICE OF ACCEPTABILITY OF WORK

PROJECT: Silver Creek 30 and 33, Burt County, Nebraska

OWNER: Papio-Missouri River Natural Resources District

CONTRACTOR:

OWNER'S CONSTRUCTION CONTRACT IDENTIFICATION:

EFFECTIVE DATE OF THE CONSTRUCTION CONTRACT:

ENGINEER: Olsson, Inc.

NOTICE DATE:

To: Papio-Missouri River Natural Resources District
Owner

And To: _____
Contractor

From: Olsson, Inc.
Engineer

The Engineer hereby gives notice to the above Owner and Contractor that that the Work furnished and performed by Contractor under the above Construction Contract is acceptable, expressly subject to the provisions of the related Contract Documents, the Agreement between Owner and Engineer for Professional Services dated September 10, 2021, and the following terms and conditions of this Notice, and that Engineer has recommended final payment of Contractor:

CONDITIONS OF NOTICE OF ACCEPTABILITY OF WORK

The Notice of Acceptability of Work ("Notice") is expressly made subject to the following terms and conditions to which all those who receive said Notice and rely thereon agree:

1. This Notice is given with the skill and care ordinarily used by members of the engineering profession practicing under similar conditions at the same time and in Nebraska.
2. This Notice reflects and is an expression of the Engineer's professional opinion.

MODIFIED VERSION of

Exhibit E – Notice of Acceptability of Work.

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one. Page 1

3. This Notice is given as to the best of Engineer's knowledge, information, and belief as of the Notice Date.
4. This Notice is based entirely on and expressly limited by the scope of services Engineer has been employed by Owner to perform or furnish during construction of the Project (including observation and/or inspection of the Contractor's work) under Engineer's Agreement with Owner, and applies only to facts that are within Engineer's knowledge or could reasonably have been ascertained by Engineer as a result of carrying out the responsibilities specifically assigned to Engineer under such Agreement.
5. This Notice is not a guarantee or warranty of Contractor's performance under the Construction Contract, an acceptance of Work that is not in accordance with the related Contract Documents, including but not limited to defective Work discovered after final inspection, nor an assumption of responsibility for any failure of Contractor to furnish and perform the Work thereunder in accordance with the Construction Contract Documents, or to otherwise comply with the Construction Contract Documents or the terms of any special guarantees specified therein.
6. This Notice does not relieve Contractor of any surviving obligations under the Construction Contract, and is subject to Owner's reservations of rights with respect to completion and final payment.

By: _____

Title: _____

Dated: _____

MODIFIED VERSION of

Exhibit E – Notice of Acceptability of Work.

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one. Page 2

Insurance

Paragraph 6.05 of the Agreement is supplemented to include the following agreement of the parties:

G6.05 Insurance

A. The limits of liability for the insurance required by Paragraph 6.05.A and 6.05.B of the Agreement are as follows:

1. By Engineer:

- | | |
|--|-------------|
| a. Workers' Compensation: | Statutory |
| b. Employer's Liability -- | |
| 1) Bodily injury, each accident: | \$500,000 |
| 2) Bodily injury by disease, each employee: | \$500,000 |
| 3) Bodily injury/disease, aggregate: | \$500,000 |
| c. General Liability -- | |
| 1) Each Occurrence (Bodily Injury and Property Damage): | \$1,000,000 |
| 2) General Aggregate: | \$2,000,000 |
| d. Excess or Umbrella Liability -- | |
| 1) Per Occurrence: | \$5,000,000 |
| 2) General Aggregate: | \$5,000,000 |
| e. Automobile Liability --Combined Single Limit (Bodily Injury and Property Damage): | |
| | \$1,000,000 |
| f. Professional Liability -- | |
| 1) Each Claim Made | \$1,000,000 |
| 2) Annual Aggregate | \$2,000,000 |
| g. Other (specify): | \$N/A |

B. *Additional Insureds:*

1. The Owner shall be listed on Engineer's general liability policy as provided in Paragraph 6.05.A.

MODIFIED VERSION of
Exhibit G – Insurance.

COI Here

This is **EXHIBIT H**, consisting of 1 page, referred to in and part of the **Agreement between Owner and Engineer for Professional Services** dated September 10, 2021.

Dispute Resolution

Paragraph 6.09 of the Agreement is supplemented to include the following agreement of the parties:

H6.08 *Dispute Resolution*

- A. *Mediation:* Owner and Engineer agree that they shall first submit any and all unsettled claims, counterclaims, disputes, and other matters in question between them arising out of or relating to this Agreement or the breach thereof ("Disputes") to mediation by a mediator to be mutually agreed upon by Owner and Engineer. Owner and Engineer agree to participate in the mediation process in good faith. The process shall be conducted on a confidential basis, and shall be completed within 120 days. If such mediation is unsuccessful in resolving a Dispute, then (1) the parties may mutually agree to a dispute resolution of their choice, or (2) either party may seek to have the Dispute resolved by a court of competent jurisdiction.

MODIFIED VERSION of

Exhibit H - Dispute Resolution.

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

This is **EXHIBIT J**, consisting of 1 page, referred to in and part of the **Agreement between Owner and Engineer for Professional Services** dated September 10, 2021.

Special Provisions

Paragraph(s) N/A of the Agreement is/are supplemented to include the following agreement(s) of the parties:

MODIFIED VERSION of

Exhibit J - Special Provisions.

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

This is **EXHIBIT K**, consisting of 2 pages, referred to in and part of the **Agreement between Owner and Engineer for Professional Services** dated September 10, 2021.

AMENDMENT TO OWNER-ENGINEER AGREEMENT

Amendment No. _____

The Effective Date of this Amendment is: _____.

Background Data

Effective Date of Owner-Engineer Agreement:

Owner: Papio-Missouri River Natural Resources District

Engineer: Olsson, Inc.

Project:

Nature of Amendment: [Check those that are applicable and delete those that are inapplicable.]

- _____ Additional Services to be performed by Engineer
- _____ Modifications to services of Engineer
- _____ Modifications to responsibilities of Owner
- _____ Modifications of payment to Engineer
- _____ Modifications to time(s) for rendering services
- _____ Modifications to other terms and conditions of the Agreement

Description of Modifications:

Here describe the modifications, in as much specificity and detail as needed. Use an attachment if necessary.

Agreement Summary:

Original agreement amount:	\$ _____
Net change for prior amendments:	\$ _____
This amendment amount:	\$ _____
Adjusted Agreement amount:	\$ _____

Change in time for services (days or date, as applicable): _____

MODIFIED VERSION of

Exhibit K – Amendment to Owner-Engineer Agreement.

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

The foregoing Agreement Summary is for reference only and does not alter the terms of the Agreement, including those set forth in Exhibit C.

Owner and Engineer hereby agree to modify the above-referenced Agreement as set forth in this Amendment. All provisions of the Agreement not modified by this or previous Amendments remain in effect.

OWNER:

ENGINEER:

Papio-Missouri River Natural Resources District

Olsson, Inc.

By: _____

By: _____

Name: John Winkler

Name: Brian Osborn

Title: General Manager

Title: Team Leader

Date Signed: _____

Date Signed: _____


MODIFIED VERSION of

Exhibit K – Amendment to Owner-Engineer Agreement.

EJCDC® E-500, Agreement Between Owner and Engineer for Professional Services, Copyright © 2014 by the National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. Those portions of the text that originated in copyrighted EJCDC documents remain subject to the copyright. A redline comparison copy highlighting the modifications will be made available upon request if you have not already received one.

Attachment 2 to Exhibit A

Time Schedule Chart

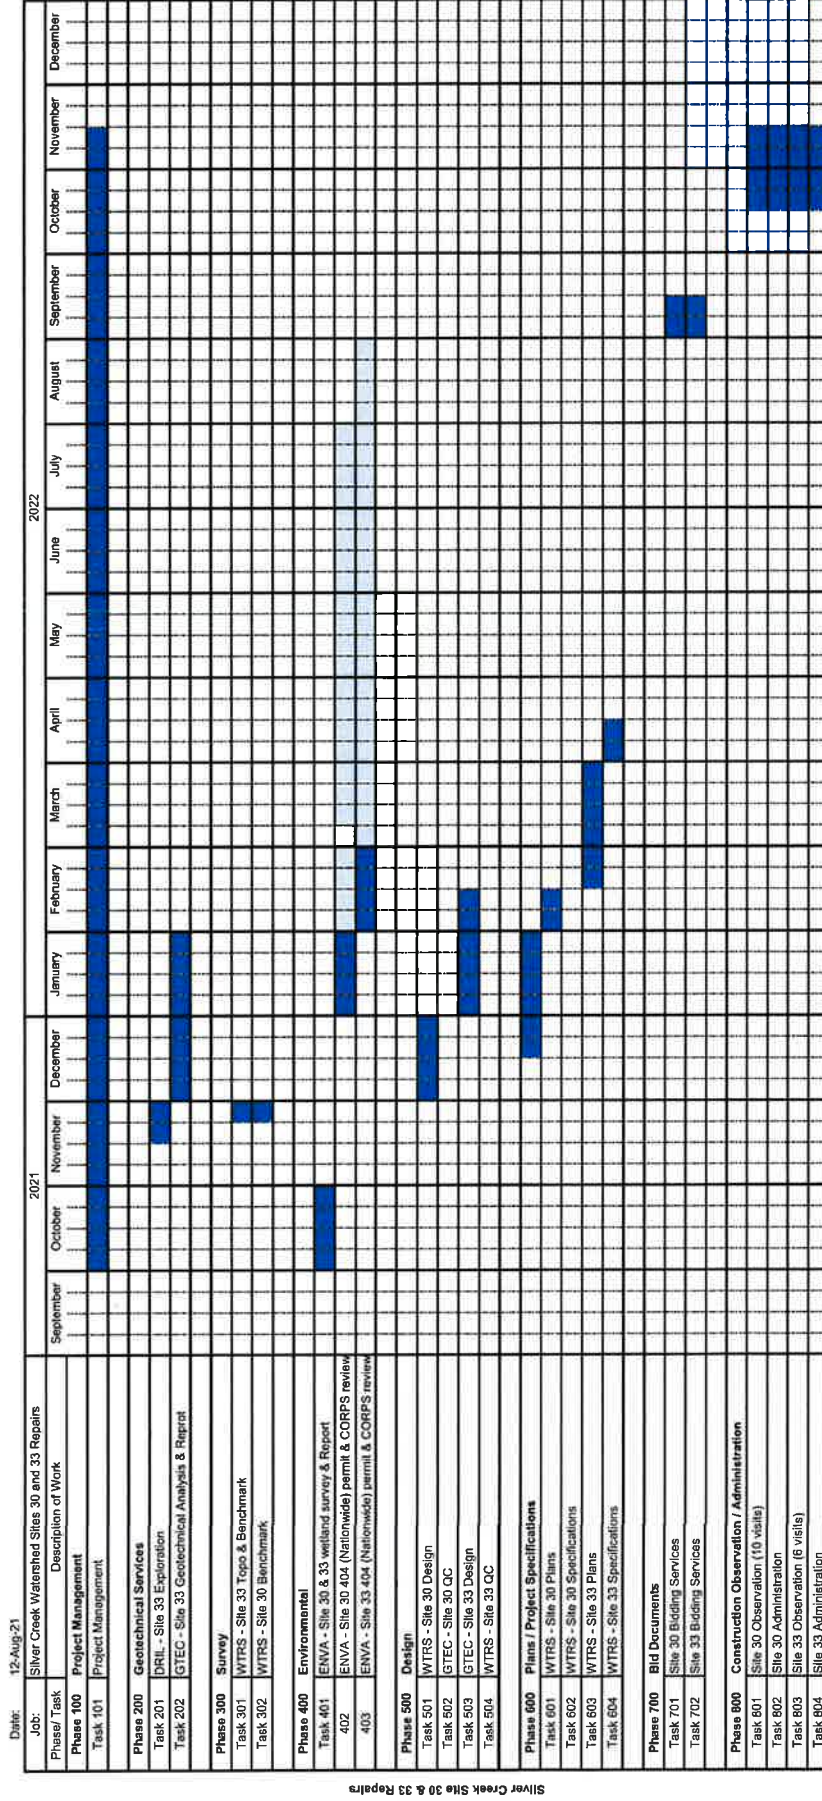

Date: Job:		Silver Creek Site 30 & 33 Repairs										LABOR/HOURS										EXPENSES										TOTALS			
Phase	Task	Principal & QA/QC	Project Manager	Design Associate	Assistant Engineer	Associate Engineer	Project Engineer	Senior Engineer	Project Scientist	Technician	Drill Crew and Rig	Construction Services	Cultural Res. Sub	Travel mile (Sub Voucher)	Travel mile (Voucher)	Mails	Phone, each	Copies, each	GPS	Title Search	Hrs Comp	Misc	Total Man-Days	Total Labor Fee	Total Expense Fee	Total Fee									
Phase 100																																			
	Task 001																																		
	Task 002																																		
Phase 100 Total		0.00	47.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00																						
Phase 200																																			
	Task 001																																		
	Task 002																																		
Phase 200 Total		0.00	0.00	0.00	0.00	44.50	33.50	10.00	0.00	0.00	10.00	0.00																							
Phase 300																																			
	Task 001																																		
	Task 002																																		
Phase 300 Total		0.00	0.00	13.25	9.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00																							
Phase 400																																			
	Task 001																																		
	Task 002																																		
Phase 400 Total		0.00	0.00	0.00	0.00	45.80	129.10	0.00	0.00	0.00	0.00	0.00																							
Phase 500																																			
	Task 001																																		
	Task 002																																		
Phase 500 Total		0.00	0.00	0.00	26.00	48.00	0.00	0.00	0.00	0.00	0.00	0.00																							
Phase 600																																			
	Task 001																																		
	Task 002																																		
Phase 600 Total																																			
Phase 700																																			
	Task 001																																		
	Task 002																																		
Phase 700 Total		0.00	0.00	0.00	26.00	56.00	0.00	0.00	0.00	0.00	0.00	0.00																							
Phase 800																																			
	Task 001																																		
	Task 002																																		
Phase 800 Total		0.00	10.00	0.00	20.00	0.00	0.00	0.00	0.00	0.00	0.00	168.00																							
GRAND TOTAL		0.00	57.00	121.00	175.00	175.00	120.00	10.00	0.00	0.00	30.00	168.00	0.00	3200.00	0.00	0.00	0.00	0.00	1.00	0.00	0.00	0.00	117.76	\$ 121,310	\$ 2,082	\$ 123,392									

